



PHASE 1.7A OF PHASE 1C NORTHERN ARC

Construction Environmental Management Plan

October 2026

Hill Group Ltd



 Transport Planning

 Travel Planning

 Civil & Structural Engineering

**RESIDENTIAL DEVELOPMENT
PHASE 1.7A OF PHASE 1C NORTHERN ARC
BURGESS HILL**

CONSTRUCTION ENVIRONMENTAL MANAGEMENT PLAN

CONTROLLED DOCUMENT

<i>Document No:</i>	1041.0010/CEMP/5	
<i>Status:</i>	Original	
	<i>Name</i>	<i>Date</i>
<i>Prepared by:</i>	Lauren Wright	June 2026
<i>Checked by:</i>	Jessica Miller	June 2026
<i>Approved by:</i>	Tom Fisher	June 2026

Revision Record

<i>Rev.</i>	<i>Date</i>	<i>By</i>	<i>Summary of Changes</i>	<i>Aprvd</i>
2	15.07.26	LJW	Updated following client comments	JAM
3	13.08.26	LJW	Updated following client comments	TAF
4	01.09.26	JAM	Updated following client comments	TAF
5	05.10.26	LJW	Amended CEMP to only relate to Phase 1.7a and Compound	TAF

Disclaimer

This document has been prepared in accordance with the scope of Paul Basham Associates Ltd's appointment with its client and is subject to the terms of that appointment. It is addressed to and for the sole use and reliance of Paul Basham Associates clients. Paul Basham Associates accepts no liability for any use of this document other than by its client and only for the purposes, stated in the document, for which it was prepared and provided. No person other than the client may copy (in whole or in part), use or rely on the contents of this document, without the prior written permission of a Director of Paul Basham Associates. Any advice, opinions, or recommendations within this document should be read and relied upon only in the context of the document as a whole. The contents of this document are not to be construed as providing legal, business or tax advice or opinion.

© Paul Basham Associates Limited



Hill Group Ltd.
The Powder House,
Gunpowder Mill,
Powdermill Lane,
Waltham Abbey,
Essex,
EN9 1BN

Paul Basham Associates Ltd
The Lambourn,
Wyndyke Furlong,
Abingdon,
Oxfordshire,
OX14 1UJ

RESIDENTIAL DEVELOPMENT PHASE 1.7A OF PHASE 1C NORTHERN ARC BURGESS HILL

CONSTRUCTION ENVIRONMENTAL MANAGEMENT PLAN

Contents

1	INTRODUCTION	2
2	SITE CONTEXT	8
3	CONSTRUCTION PROGRAMME AND METHODOLOGY.....	12
4	PUBLIC LIASON.....	16
5	VEHICLE ROUTING STRATEGY	17
6	ESTIMATED VEHICLE MOVEMENTS.....	21
7	STRATEGIES TO REDUCE IMPACT	22
8	IMPLEMENTATION, MONITORING AND UPDATING	30

Figures

- Figure 1: Phase 1C (Wider Site) Indicative Site Boundary
- Figure 2: Parcel 1.7A and Construction compound Site Boundary
- Figure 3: Personal Injury Collision Locations
- Figure 4: Construction Traffic Routes

Tables

- Table 1: Requirements of Condition 8 of Outline Planning Application
- Table 2: Construction Particulars
- Table 3: Parcel 1.7A Phasing Duration (extracted from Burgess Hill Tender Programme)

Appendices

- Appendix A – CEMP Consultation Comments from Environmental Protection, Highways and Ecology
- Appendix B – Phase 1C Proposed Illustrative Masterplan
- Appendix C – Parcel 1.7A Site Layout and Construction Compound Layout
- Appendix D – Burgess Hill Tender Programme
- Appendix E – Vehicle Tracking
- Appendix F – Ecology Statement for Parcel 1.7A and the Construction Compound

1 INTRODUCTION

Background

1.1 This Construction Environmental Management Plan (CEMP) has been prepared by Paul Basham Associates on behalf of Hill Group Ltd. This CEMP supports the Reserved Matters permission of Phase 1C of the Burgess Hill Northern Arc development that was granted planning consent on 26th March 2026 (reference DM/25/1986), however this CEMP only refers to Parcel 1.7A and the construction compound of Phase 1C. The whole of Phase 1C forms part of the wider outline consented Northern Arc development, to the north of Burgess Hill in West Sussex (reference DM/18/5114).

1.2 The Proposed Development of this Reserved Matters application of Phase 1C is set out below:

Consideration of access, appearance, landscaping, layout and scale for parcels 1.7a, 1.7b, 1.8 and OS1.8 comprising:

- a) Eastern Neighbourhood Centre: Up to 270 residential dwellings and extra care units; commercial floorspace; the community building, the neighbourhood square, cycle and pedestrian connections, parking and associated infrastructure.*
- b) Eastern Parkland comprising open space, multi-use games areas (MUGA), public art, green circle cycle link and associated infrastructure.*

1.3 This CEMP has been prepared specifically for the development of Parcel 1.7A and the construction compound, with another CEMP to be prepared and submitted at a later stage specific to the remaining Parcels 1.7b, 1.8 and OS1.8. The development quantum of Parcel 1.7A comprises a total of 115 dwellings split between 37 apartments and 78 houses.

1.4 An Outline CEMP was prepared by AECOM in 2018 for the wider Northern Arc outline application (document reference: Appendix 5.1 of Environmental Statement Volume II). The Outline CEMP “provides an overarching strategy for the management of environmental effects and the implementation of measures prior to, and during, the demolition and construction phase of the Proposed Development”. The Outline CEMP includes a guiding framework for the measures that will be adopted and implemented by Hill Group and their Principal Contractor, during the construction of this Proposed Development, which are set out in this detailed CEMP.

1.5 Within the Environmental Statement Volume I, also prepared by AECOM in 2018 for the wider Northern Arc outline application, ‘Chapter 16 Mitigation Register’ sets out various mitigation measures that were identified during the Environmental Impact Assessment (EIA) and how the mitigation will be secured. Some of the measures were classed as ‘tertiary mitigation’ which are considered standard practice, of which these were stated as being secured through the planning condition requiring the preparation of

a CEMP for the relevant reserved matters applications. Chapter 7 of this detailed CEMP covers the appropriate measures of the Mitigation Register that were informed to be included in the CEMP.

- 1.6 For the Reserved Matters permission, Transport Planning consultancy services have been provided by GTA Civils and Transport who prepared a Transport Assessment Addendum (November 2025, document reference: 12824 Transport Assessment Addendum 4th Issue) and a Highways Technical Note (November 2025, document reference: 12824 Technical Note on Layout 1st Issue). This CEMP references where relevant, both these documents, and should be read in conjunction with them.
- 1.7 Within the Pre-Commencements Conditions attached to the wider Outline Planning Permission, Condition 8 states “prior to the commencement of development within each reserved matters area, a Construction Environmental Management Plan (CEMP) shall be submitted to and approved in writing by the Local Planning Authority in respect of development within that Reserved Matters area”. The condition also sets out a list of details that need to be included within the CEMP, which are set out in **Table 1**.
- 1.8 The Decision Notice approving the Reserved Matters application did not attach a condition relating to the submission of a CEMP, however it referred to the need for the Mid Sussex District Council Construction Charter for Developers to be adhered to.

Condition Bullet point	Details that shall be included within the CEMP	Location in this CEMP
8.1	The appropriate Mitigation Measures stated as being contained within the CEMP in Table 16-1 'Summary of Mitigation Measures from within the Technical ES Chapters', Chapter 16 Mitigation Register, of the Environmental Statement Volume 1 (December 2018)	Chapter 7
8.2	Setting out avoidance and mitigation measures in respect of wildlife and habitats	Chapter 7
8.3	A timetable for the commencement, construction, occupation and completion of the development	Chapter 3
8.4	The anticipated number, frequency and types of vehicles used during construction	Chapter 6
8.5	The method of access and routing of vehicles during construction and directional signage for the purposes of such	Chapter 5
8.6	The siting and layout of site compounds and welfare facilities for construction workers	Chapter 3
8.7	The provision of parking of vehicles by site operatives and visitors	Chapter 5
8.8	The provision for the loading and unloading of plant, materials and removal of waste	Chapter 3
8.9	The provision for the storage of plant and materials used in construction of the development	Chapter 3
8.10	The design, erection and maintenance of security hoardings and other measures related to site health and safety	Chapter 3
8.11	Hours of construction working	Chapter 3
8.12	Details of construction lighting	Chapter 3
8.13	Measures to monitor and control noise and vibration affecting nearby residents;	Chapter 7
8.14	The provision of wheel washing facilities and other works required to mitigate the impact of construction upon the public highway, including the provision of	Chapter 5

Condition Bullet point	Details that shall be included within the CEMP	Location in this CEMP
	temporary Traffic Regulation Orders	
8.15	Dust control measures	Chapter 7
8.16	Pollution incident control and site contact details in case of complaints	Chapter 4 and 7
8.17	A scheme for community liaison and public engagement during construction, including the provision of information to occupiers moving onto the site before the development is complete	Chapter 4
8.18	Contact details of site operations manager, contracts manager, and any other relevant personnel	Chapter 2

Table 1: Requirements of Condition 8 of Outline Planning Application
DM18/0569 for the Burgess Hill Northern Arc Development

Purpose of CEMP Revisions

- 1.9 As seen in the document control revision record, previous iterations of this CEMP have been prepared, and the first CEMP submitted to MSDC was CEMP Revision 3, submitted on 20th September 2026 (referred hereafter to as CEMP3). A consultation response was received from the MSDC Environmental Protection Team on 26th September (shown in **Appendix A**) regarding CEMP3 which stated clarification of the intended approach to noise and vibration management should be provided, in addition to further clarification being needed on the weekday construction working hours, as they were shown to be from 8am to 8pm, rather than the normal hours of 8am to 6pm.
- 1.10 CEMP Revision 4 (CEMP4) was therefore prepared to resolve the comments set out above from the Environmental Protection Team, through including further information on noise and vibration management, and the amending of the weekday construction working hours in the CEMP to being between 8am to 6pm, which is in line with normal working hours. CEMP4 was subsequently MSDC on 2nd September 2026, where both CEMP3 and CEMP4 related to all parcels within the Phase 1C development.
- 1.11 West Sussex County Council (WSSCC) Highways provided a consultation response on 2nd September 2026 (shown in **Appendix A**) in which they requested further information to be provided: confirmation on the number of subcontractors anticipated on site, clarification on the parking provision and any additional parking, and the location of wheel washing facilities should be identified.
- 1.12 Place Services, on behalf of MSDC, provided an Ecology consultation response on 11th September 2026 (shown in **Appendix A**) which said there was also additional ecology information required before the condition can be satisfied. The Ecology Consultant considered the ecology mitigation measures presented in CEMP4 were not robust enough to demonstrate protection of irreplaceable habitat, protected and priority species/habitats. The Consultant further recommended the applicant's Suitably Qualified Ecologist should include detailed ecological measures within the CEMP.

- 1.13 The MSDC Planning Officer acknowledged in the covering email when sharing the Ecology comments that there are number of further ecology surveys to be undertaken during the appropriate survey seasons. The Planning Officer also stated the Condition 8 of the Outline Consent could be discharged in relation to individual parcels, particularly if there are certain parcels that do not require further survey works to be carried out, as shown on the email in **Appendix A**.
- 1.14 There are no further ecology survey works needed to be carried out for the development of Parcel 1.7A, therefore, in response to the recommendations set out above, the applicant is proceeding to submit this CEMP Revision 5 (CEMP5) solely relating to the development of Parcel 1.7A and the construction compound. Another CEMP will be submitted at a later stage in relation to the outstanding parcels of Phase 1C.
- 1.15 CEMP5 addresses and resolves comments raised both by WSCC Highways and Place Services Ecology Consultants, with revised information set out in Sections 6 and 7 of this CEMP. CEMP5 now only relates to Parcel 1.7A and the construction compound.
- 1.16 This CEMP has been prepared in accordance with the Outline CEMP (2018), Condition 8 of the outline consent, and the Construction Charter for Developers included in the Reserved Matters Decision Notice. Therefore, the submission of this CEMP seeks to partly discharge Condition 8 of the outline consent, to enable the development of Parcel 1.7A for 115 dwellings and the construction compound to begin.

Planning History

- 1.17 The outline planning consent for the wider Northern Arc development was granted on 4th October 2019, for the development description as set out below:
- “Comprehensive, phased, mixed-use development comprising approximately 3,040 dwellings including 60 units of extra care accommodation (use class C3) and 13 permanent gypsy and traveller pitches, including a centre for community sport with ancillary facilities (use class D2), three local centres (comprising use classes A1-A5 and B1, and stand-alone community facilities within use class D1), healthcare facilities (use Class D1), and employment development comprising a 4 hectare dedicated business park (use classes B1 and B2), two primary school campuses and a secondary school campus (use class D1), public open space, recreation areas, play areas, associated infrastructure, including pedestrian and cycle routes, means of access, roads, car parking, bridges, landscaping, surface water attenuation, recycling centre and waste collection infrastructure with associated demolition of existing buildings and structures, earthworks, temporary and permanent utility infrastructure and associated works.”*

- 1.18 Development of the full Northern Arc is expected to be phased over a period of 15 years, where Phase 1A (the separately consented Freeks Farm development, reference DM/18/0509), Phase 1B (reference DM/21/3870) and a new single carriageway link road known as Northern Arc Eastern Bridge Link Road (EBLR, reference DM/19/3313) have all received planning consent and are currently under construction.
- 1.19 Each of these applications have prepared and submitted detailed CEMPs to discharge planning conditions. These CEMPs have been reviewed in the preparation of this Phase 1C CEMP to ensure a consistent approach is taken to mitigating construction environmental effects across the developments.

Construction Particulars

- 1.20 The details of this CEMP and the development are set out in **Table 2**.

Site Address	Land East of Isaacs Lane, Burgess Hill, West Sussex, RH15 8RA
Contractor	To Be Confirmed
Site Working Days	Monday to Friday & Saturdays No bank holidays or Sundays
Site Working Hours	Monday to Friday: 08:00 – 18:00 Saturday: 08:00 – 13:00 Sunday and Bank Holidays: No Works
CEMP Author	Paul Basham Associates info@paulbashamassociates.com
24-hour contact information	Justin Brown, Contracts Manager for Site – JustinBrown@hill.co.uk

Table 2: Construction Particulars

Relevant Policy

- 1.21 Within the Decision Notice for the development of Phase 1C, the Mid Sussex District Council ‘Construction Charter for Developers’ was included as an attachment. The Charter sets out expectations for developers to adhere to on all sites, of which this CEMP will ensure that these are met.
- 1.22 The 6 key expectations within the Construction Charter are set out as follows:

1. Stick to your planning permission

Your planning permission has been granted for a specific development (as per the approved plans) and will be subject to conditions and maybe legal agreements. The Council and the local community expect you to stick to these and to give advance notice if anything needs to be changed.

2. Be safe and tidy

Carry out all works with the utmost care for the safety of passers-by as well as your workers, this includes driving vehicles on and off the site. Keep all plant and machinery in safe working order, and all structures safe, by checking them often. Keep your site and roads and pavements around it tidy

3. Be considerate

Carry out all work with consideration for residents, workers, pedestrians, visitors, neighbours, businesses and road users, at all times and with every effort to minimise noise and disturbance. Pay special attention to the needs of those who have difficulties with sight, hearing or mobility, and those in wheelchairs or with prams and pushchairs.

4. Be responsible

It is the responsibility of the main contractor to ensure that all employees, agents, subcontractors, suppliers, drivers and others working on or near the site comply with this Code of Practice. Please note that all sites are responsible for damage made to the public highway as a result of construction activity. Contractors carrying out the work resulting in damage are liable for the full cost of repair.

5. Be accountable

Display a contact board outside the site, giving names and telephone numbers of staff who can easily be contacted to respond to the concerns of residents, businesses and others.

6. Communicate

Keep residents and others informed about unavoidable disturbance such as noise, dust, extended working hours and disruption of traffic. Provide site neighbours with clear information well in advance of starting works, preferably in writing, and perhaps issue regular bulletins about site progress.

Report Structure

1.23 Following this introduction, this CEMP covers the following:

- Site context;
- Construction programme and methodology;
- Vehicle routing strategy;
- Estimated vehicle movements;
- Strategies to reduce impacts; and
- Implementing, monitoring and updating.

2 SITE CONTEXT

Site Location

- 2.1 The location of the Proposed Development is referred to as Parcel 1.7A and the associated construction compound of Phase 1C of the larger Northern Arc development. The Northern Arc development is a strategic urban extension spanning between the Bedelands Nature Reserve on the east of Burgess Hill, to the Goddards Green Treatment Works to the west. The indicative site boundary of Phase 1C of the Northern Arc development is shown below in **Figure 1**, with the wider site Proposed Illustrative Masterplan shown in **Appendix B**. The location of Parcel 1.7A and the construction compound that this CEMP has been prepared for are shown below in **Figure 2**, with the Site Layout Plan and Construction Compound Layout shown in **Appendix C**.
- 2.2 Approximately half of the Phase 1C site has been used for access and construction related purposes for the new Eastern Bridge Link Road (EBLR), as also seen in the aerial imagery below.



Figure 1: Phase 1C (Wider Site) Indicative Site Boundary



Figure 2: Parcel 1.7A and Construction compound Site Boundary

Local Road Network

- 2.3 The site is located off the A273 Isaac's Lane that forms the western boundary of the site. To the south of the site, the A273 Isaac's Lane becomes the A273 Sussex Way/Jane Murray Way, at the Fairplace Hill North and South Roundabouts. The A273 Sussex Way and Jane Murray Way form the western ring road around Burgess Hill. To the north, the A273 connects Burgess Hill to Haywards Heath at the Bolnore Roundabout with the A272 and Parkfield Way.
- 2.4 The A273 is a single carriageway road, where the extent north of the site is subject to a 50mph speed limit, which then reduces to 40mph adjacent to the Phase 1C site boundary. Isaac's Lane is unlit and currently has no pedestrian footway on either side of the carriageway.
- 2.5 The A273 Sussex Way benefits from street lighting and a pedestrian footway on the southern side of the carriageway, and is also subject to a 40 mph speed limit.
- 2.6 The B2036 is also located near the site, off the Fairplace Hill North Roundabout, that connects Burgess Hill in the south to Ansty in the north, at the junction with the A272. The B2036 is a single carriageway road subject to the national speed limit.

Strategic Road Network

- 2.7 The A23 which runs between London and Brighton is located approximately 4.5 miles to the west of the site, accessed via the A273 and the A2300. The A23 is part of the Strategic Road Network (SRN) and is

managed by National Highways. To the south, at Brighton, the A23 connects with the east-west A27 that runs between Eastbourne and Portsmouth. To the north, the A23 connects with the circular M25, or continues into London.

Personal Injury Collision Assessment

- 2.8 To understand if there are any existing collision clusters which could potentially be impacted by an increase in construction vehicles within the vicinity of the site, Personal Injury Collision (PIC) data has been obtained from the Department for Transport's Mapping Application for Visualising Road Injury Casualties (MAVRIC). PIC data for the latest five-year period available, which is between 2019 and 2024, has been reviewed and the locations of any collisions recorded has been illustrated within **Figure 3**.

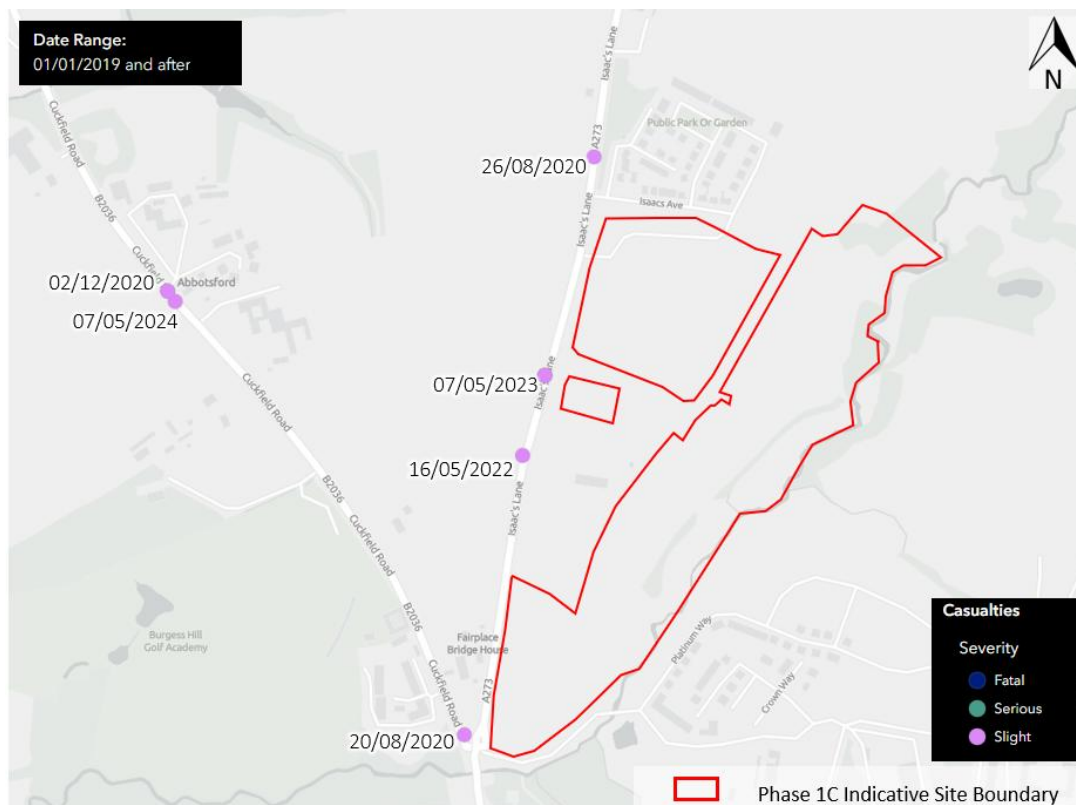


Figure 3: Personal Injury Collision Locations

- 2.9 The PIC review identified three 'slight' collisions within the vicinity of the site on the A273 Isaac's Lane which occurred in August 2020, May 2022 and May 2023. At the time of these collisions, the southern part of the A273 (between Isaac's Avenue and the Fairbridge Hill North Roundabout) had a 60 mph speed limit, and the A273 north of Isaac's Avenue had a 50 mph speed limit. To note, these collisions did not occur near junctions, and since the construction of Phase 1B off Isaac's Lane began in 2024, the junctions of Isaac's Avenue and Holmbush Avenue have been constructed whilst the speed limit for this extent of the road has been reduced to 40 mph, therefore improving highway safety.

- 2.10 There were three 'slight' collisions recorded on the B2036 Cuckfield Road, one of which occurred at the Fairfield Hill North Roundabout in August 2020, and two occurred in Abbotsford near the junction with Hook Place.
- 2.11 It can be concluded that the highway safety of the A273 has been improved since the reduction of the speed limit, and there were no other locations of significant collision clusters identified that would be made worse by the construction traffic associated with the Proposed Development.

Proposed Development Details

- 2.12 The development quantum of Parcel 1.7A includes:
- 115 dwellings comprised of:
 - 37 apartments,
 - 78 houses.

Access Arrangements

- 2.13 Parcel 1.7A will be accessed by the newly constructed Eastern Bridge Link Road (EBLR), now named Holmbush Avenue, which bisects the A273 at a new signalised T-junction. Holmbush Avenue is subject to a 30 mph speed limit, with internal local roads off Holmbush Avenue subject to a lower design speed of 20mph. The A273 currently has a 40mph speed limit, but it is anticipated this will be reduced to 30mph as the rest of the Northern Arc development comes forward.
- 2.14 Holmbush Avenue becomes Eastbridge Avenue through the Freeks Farm development to the east of Phase 1C, which then connects onto Maple Drive to the southeast, providing a secondary access to the development.
- 2.15 The EBLR is also referred to as the Green Superhighway, where it will be a tree lined avenue with segregated cycle/footway facilities provided on both sides of the road for sustainable transport connections, set back from the carriageway by a verge on either side.
- 2.16 The development internal road layout has been designed to allow for accessibility and turning movements of all vehicles including fire appliances and refuse vehicles.

3 CONSTRUCTION PROGRAMME AND METHODOLOGY

Construction Phasing

- 3.1 A detailed construction programme for the whole of Phase 1C has been prepared by the client, and the programme for Parcel 1.7A can be seen within the 'Burgess Hill Tender Programme' that is included in **Appendix D**. This programme sets out each phase of pre-construction works, site enabling works and construction works, along with the duration, start and end of each phase.
- 3.2 Enabling works started on site on 5th October 2026, with the different parcels of land being developed generally sequentially, but there will be stages where works are going on different parcels at the same time. A summary of the different phases of the project, along with the duration, and start and end dates of each phase has been shown below in **Table 3**.

Phase	Duration (rounded up to nearest whole week)	Phase Starts	Phase Ends
Enabling Works	4	05 October 2026	30 October 2026
Ground Works	42	19 October 2026	6 August 2027
Infrastructure	52	02 November 2026	27 October 2027
Parcel 1.7A (37 apartments & 78 houses)	94	16 November 2026	29 August 2028

Table 3: Parcel 1.7A Phasing Duration (extracted from Burgess Hill Tender Programme)

Construction Working Hours

- 3.3 The core hours for demolition and construction will be:
- Monday to Friday 08:00 hours to 18:00 hours;
 - Saturday 08:00 hours to 13:00 hours;
 - No working normally undertaken on Sundays, Bank or Public Holidays (unless agreed in advance with MSDC and Homes England).
- 3.4 All work outside these hours will be subject to prior agreement of, and/ or reasonable notice to MSDC and Homes England as appropriate. Night-time working will be restricted to exceptional circumstances, and work internally within buildings. By arrangement, there may be some out of hours construction deliveries made to the Site.
- 3.5 The Principal Contractor may require a period of up to one hour before and one hour after core working hours for start-up and close down activities. Activities will not include the use of plant or machinery likely to cause disturbance to neighbouring residents/businesses but may include deliveries, movement to place of work, unloading, maintenance and general preparation works.
- 3.6 In the case of work required in an emergency, or which if not completed would be unsafe or harmful to workers, the public or local environment, MSDC and Homes England will be informed as soon as

reasonably practicable of the reasons and likely duration. Examples may include: concrete pouring taking longer than anticipated due to unfavourable conditions or equipment failure.

Welfare Compound

- 3.7 Prior to works commencing, a welfare compound with facilities such as a site office and toilets will be created. The welfare compound location will be highlighted on the logistics pack, and will be provided throughout the construction stages, and will be removed from site after construction is finalised to allow for the completion of external landscaping works. The construction compound layout plan is attached as **Appendix C**, whilst the exact site layout shown in this plan may be subject to further changes, the compound location and overall size will remain unchanged.

Deliveries

- 3.8 The hours of delivery are intended to be the same as the construction working hours as set out above. As part of the supply chain pre-qualification questionnaire and tender process deliveries of all materials will conform to these hours.
- 3.9 The Principal Contractor will co-ordinate all deliveries and collections to/from the Site, and ensure that as far as possible:
- All delivery and collection vehicles connected with the Site are aware of the vehicle routing;
 - Prior to a delivery or collection, if required, hauliers will notify the relevant authorities (MSDC, Highways Authority, etc.) in accordance with the Road Vehicles (Authorisation of Special Types) (General) Order 2003 (Ref. 3); and
 - Deliveries will be made on a 'just in time' basis.
- 3.10 Larger vehicle movements will be scheduled to avoid peak hours on the local road network, where possible. If an alternative construction traffic route is required for any reason, this will be agreed in advance with MSDC and Homes England.
- 3.11 A pre-booking system for deliveries will be implemented and managed so as to ensure minimal impact to the free flow of traffic on the public highways. The majority of unloading will take place within the materials storage area located within the main compound. If for any reason it is necessary to load and unload outside the Site boundary, the details and procedure for this will be agreed in advance with MSDC and Homes England.
- 3.12 All suppliers will be instructed to deliver to the site from the A237 Issacs Lane, as set out further in the vehicle routing strategy. Localised signage will be installed directly outside the development and leading to the materials storage area.

- 3.13 Deliveries to the Site will be controlled to avoid congestion of the surrounding roads. The logistics manager will produce a rolling weekly programme of deliveries and a draft of this programme will be presented and discussed at weekly progress meetings to smooth out obvious bottlenecks and clashes. Where possible, deliveries will be taken on Site early to allow the vehicles to be offloaded during the peak period and then leave the Site once the peak period has ended. This will allow greater efficiency in predicting delivery times and reduces haulage costs. Similarly, the latest delivery to Site will be scheduled to ensure that it can be offloaded by 18:00 and that the vehicle leaves the Site as the evening peak is subsiding. The Site will be closed up in accordance with the working hours.

Site Hoardings

- 3.14 The perimeter of the site will be secured by hoardings for site security and public safety. These hoardings will be 3m high (barrier from ground level) complying with British Standard (BS) 5975 (Ref. 1) for construction of temporary works.

Storage of Materials

- 3.15 All materials will be stored within the site boundary in the dedicated materials storage area, which will not encroach on the highway. There will also be satellite material storage areas within the construction parcels where available.

Lighting

- 3.16 The welfare compound will be lit with PIR lighting. Additional lighting along walkways and construction lighting to construction zones will also be provided.
- 3.17 Low wattage directional lighting will be used on the Site during the demolition and construction works to avoid lighting disturbance of neighbouring land uses, in line with the Institute of Lighting Engineers 'Guidance Notes for the Reduction of Obtrusive Light' (Ref. 2). Lighting will be provided with the minimum luminosity sufficient for safety and security purposes. Where practicable, precautions will be taken to avoid shadows cast by the site hoarding on surrounding footpaths, roads and amenity areas.
- 3.18 Where practical, motion sensor lighting and low energy consumption fittings will be installed to reduce usage and energy consumption.
- 3.19 The construction schedule activities will be primarily kept to daylight hours and the use of high powered floodlights during hours of darkness will be limited.

3.20 It is assumed that lighting for construction and operation phases will adhere to the following recommendations:

- New lighting for the Proposed Development will respond to the British Standards and good practice guidance to support safe access and use of the Site;
- All lighting is to be aimed at its intended target, away from neighbouring properties and identified habitats or commuting routes which include: trees, hedges, rivers, ponds and bat/bird flight zones;
- When possible, full cut-off luminaires will be used and shields, hoods, cowls, baffles or louvres will be employed to aid in further control of new lighting near sensitive areas to limit upward light or direct views of light sources;
- New permanent or temporary lighting near sensitive ecological receptors should limit the output of blue and ultraviolet range to avoid damage to insects behaviours and lighting levels and temperature on different species of bats; and
- It is assumed that all lighting applications within the Proposed Development are not required through the hours of darkness. Lighting equipment will be switched off, or lighting with the capability to is to be dimmed, in accordance with West Sussex County Council (WSSCC) approved strategies for part night lighting.

4 PUBLIC LIASON

Community Engagement

- 4.1 The contractor will seek to actively engage with all relevant stakeholders throughout the construction programme. It is anticipated that the contractor will issue advisory notes and leaflets to local households, businesses and community facilities to keep them informed of upcoming and ongoing works.
- 4.2 The public will be provided with all contact details of the principal contractor, who will have a dedicated customer liaison team. All queries and complaints received will be dealt with by the customer liaison team, who in addition will keep a register of all complaints.

On-site Logistics Manager

- 4.3 The contractor will designate a member of on-site staff to assist with the management of traffic, pedestrians and cyclists when construction vehicles are arriving and departing the site to ensure safety.

5 VEHICLE ROUTING STRATEGY

Vehicle access arrangements at site access

- 5.1 All construction vehicles will follow pre-determined routes to ensure drivers only use routes appropriate to their vehicle type.
- 5.2 Vehicles will be instructed to enter the site from Isaac's Lane with localised signage to be installed directly outside the development and lead to the materials storage area.
- 5.3 Tracking of an HGV accessing and egressing the site has been shown in **Appendix E**. Swept paths for a standard car have also been demonstrated, indicating the HGV movements do not impede on the ability for cars to continue their respective movements.

Vehicle Routes

- 5.4 **Figure 4** shows the construction traffic routes to the Site. Access routes to and from the Site to be utilised by HGVs, and the Site access points will be agreed with MSDC and Homes England prior to the start of the demolition and construction works.

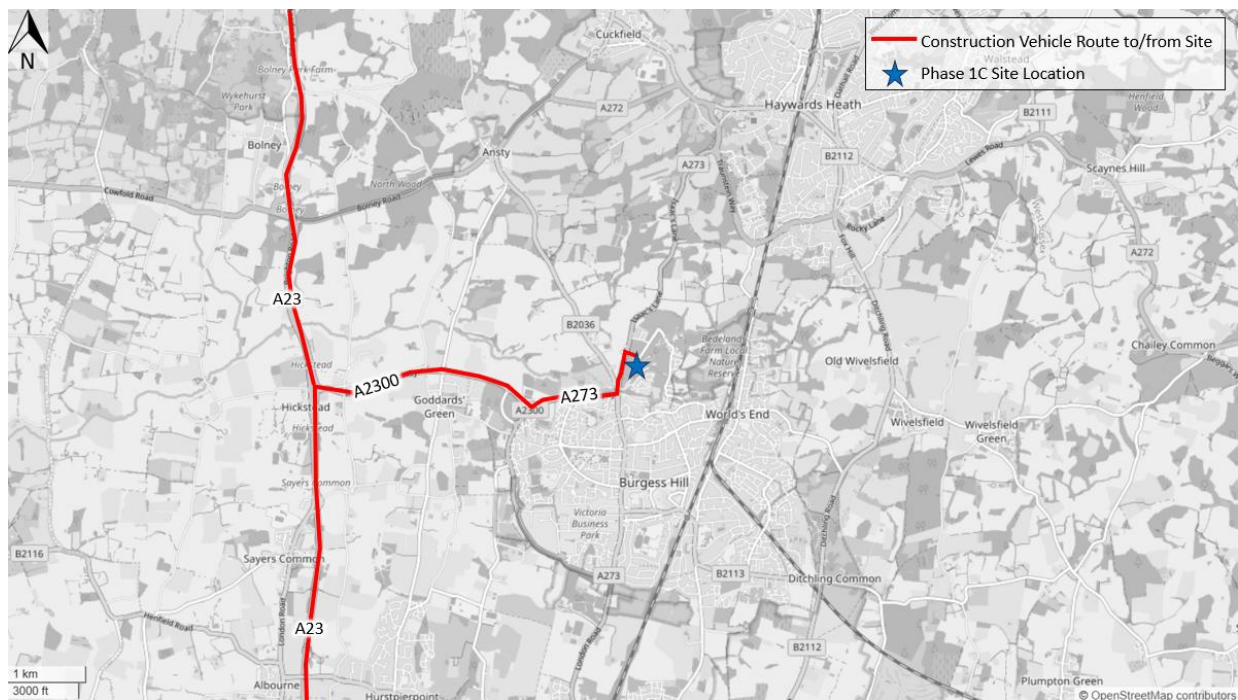


Figure 4: Construction Traffic Routes

- 5.5 Construction traffic will be routed to the site from the wider highway network via the M23, A23, A2300, and the A273. Access for construction traffic will be segregated from operational traffic wherever practicable.

- 5.6 Temporary construction signage will be agreed with West Sussex County Council (WSSCC) and erected prior to works commencing and any temporary traffic management requirements will be agreed in advance with WSSCC.
- 5.7 It is anticipated that traffic flows would generally take place out of peak hours when congestion on the local road network is lower. Deliveries will also be timed to avoid peak periods of traffic, particularly times and locations where children will be moving to or from school. The anticipated peak periods of activity and movement of HGV vehicles would coincide with the superstructure construction.
- 5.8 It is anticipated that the largest vehicles accessing the Site will be ready mix concrete trucks and flatbed lorries carrying of bricks, steel posts, beams and timber. These will be managed through the Principal Contractor.

Parking Provision

- 5.9 There will be a subcontractor parking area located adjacent to the welfare compound within the site, which can accommodate up to 24 vehicles. This number of parking spaces has been determined based on other subcontractor parking areas that have been provided on other schemes of similar sizes by the Primary Contractor. From the outset, contractors will be requested to car/van share where possible, to reduce the number of vehicle movements to and from site, with all parking to be managed by the Site Manager. The construction of the site will be a phased approach, therefore there is the ability to minimise the total number of trades and subcontractors on site at any one time. Additionally, as on-site parking becomes available within the Parcel (i.e. driveways and laybys on the private roads), these will act as additional parking should it be needed.
- 5.10 There may be times where the parking area cannot accommodate all subcontractor vehicles, therefore in those instances contractors will be advised to 'park and ride', where they can park at the Burgess Hill train station car park or Market Place Shopping Centre car park for the day and get on the new 38 Bus Service to the site. The 38 bus service is a circular route from the town centre to the development along Holmbush Avenue and Eastbridge Avenue, with the journey taking approximately 10 minutes on the bus each way.
- 5.11 In the occurrence that contractors may have to park off-site, should the site car park be full and/or they cannot use the bus to get to site, they will have find their own parking, avoiding roads within the immediate local area but ensuring compliance with local traffic management regulations and parking restrictions. If contractors have to park off-site, this will be managed by the Site Manager to ensure that any overspill parking does not result in obstructions to existing users of the highway network.

- 5.12 Details of any parking requirements for abnormal or large loads, in connection with the development, are to be provided in advance by the Primary Contractor and routing and timing is to be agreed in advance with MSDC and Homes England.
- 5.13 Parking in other areas of the site development, apart from those signed as being for car parking (which will be located within the compound area), such as on the site access roads will not be permitted.

Vehicle Management

- 5.14 The Primary Contractor will control all deliveries and traffic entering and exiting the site. Contractors will be required to maintain clear and safe pedestrian access to all office accommodation, and maintain existing easements, access and egress.
- 5.15 On site routes are restricted to a maximum speed limit of 6 mph. Hill Group will impose a lower speed limit of 4mph for all vehicles travelling over unmade ground to minimise the likelihood of dust raising. These speed limits apply to all vehicles at all times.

Vehicle Wheel Washing

- 5.16 The Principal Contractor will take strict measures to minimise the spillage of mud arising from the demolition and construction works onto the roads adjacent to the Site.
- 5.17 In the early stages of the demolition and construction works, the Principal Contractor will install a wheel washing facility, to ensure that mud/detritus originating from the Site is not deposited on the public highway. Where utilised, a wash bay area will be impermeable and isolated from the surrounding area by a raised kerb or roll over bund to contain solids, with effluent directed to the foul sewer via a silt buster or other settlement technology and subject to discharge consent.
- 5.18 The location of the wheel washing facility will be on the access point off Holmbush Avenue into the Parcel, adjacent to the location of the construction compound.
- 5.19 Where mud/ detritus is observed being tracked on the highway from the Site, the Principal Contractor will make arrangements for it to be cleaned up (e.g. road sweeping).
- 5.20 No vehicles will be permitted to leave Site if it is considered that these may pose a risk to the public highway. Vehicles carrying loads with the potential to deposit mud or other debris will be fully sheeted to minimise the risk of any mud spilling onto the highway.

5.21 Watering down of the Site will be carried out as required to suppress dust on:

- Unpaved areas that are subject to traffic or wind;
- Sand, spoil and aggregate stockpiles; and
- During loading/unloading of dust-generating materials.

6 ESTIMATED VEHICLE MOVEMENTS

Construction Delivery Vehicles

- 6.1 There will be a maximum of between 15 to 20 construction vehicles making deliveries to the site per day, Monday to Saturday, which will be spread across the working day. These will be a mix of vehicle sizes and will include HGVs.
- 6.2 As set out in the construction vehicle routing plan, all construction deliveries to the site must arrive to the site from the A273 Isaacs Lane, not via Eastbridge Avenue.
- 6.3 As set out previously, these deliveries will be scheduled to arrive throughout the day within the defined construction hours, therefore reducing the impact of congestion that can be caused by construction vehicles on the local road network.

Subcontractor Vehicles

- 6.4 There will be on average, 50 to 60 subcontractor vehicles per day arriving to the site. It will be highlighted during inductions that subcontractors should where possible, arrive and leave site before or after the morning and evening peak hours. It is important to note this is the absolute peak number of vehicles anticipated on-site during the busiest time of the build, which includes visitors for client meetings, which would only be once per month for such visits.
- 6.5 There will be car parking provided next to the welfare compound, and additional lay down parking areas will be installed as the build progresses should they be required to avoid any subcontractors parking on Holmbush Avenue or Issacs Avenue.

7 STRATEGIES TO REDUCE IMPACT

Overview

- 7.1 This section describes the measures that will be implemented to ensure the CEMP is effective in achieving the aims of reducing environmental impact, road risk, congestion and cost. These measures align with those set out in the Outline CEMP and the other CEMPs that have been produced for the Northern Arc development thus far.

Safety and Environmental Standards

- 7.2 The Principal Contractor will be a member of the Considerate Constructors Scheme (CCS) which plays a valuable role in improving health and safety standards and working practices across the construction industry.
- 7.3 The Principal Contractor will aim to meet the Construction Logistics and Community Safety (CLOCS) standard for construction logistics. By being recognised as a member of FORS, the Principal Contractor will already demonstrate several requirements to meet the CLOCS standard. Any additional requirements such as driver training will be agreed on the award of contracts.
- 7.4 The Principal Contractor will use contractors who are members of the Fleet Operators Recognition Scheme (FORS), wherever possible. FORS provides a quality and performance benchmark for the industry.
- 7.4.1 A member of the construction team will be appointed to manage vehicle movements in and out of the site and record any operational incidents.
- 7.4.2 All staff on site will be required to wear Personal Protective Equipment (PPE), including visitors and a Health and Safety Plan will be prepared for the site.

Adherence to Designated Routes

- 7.5 All construction related traffic and deliveries will be carefully managed to ensure that journeys to and from the site adhere to agreed routes along the SRN and local roads. The proposed routes are identified in Section 5 and will be agreed to minimise the impact of the works on the surrounding highway network and local communities.
- 7.6 Copies of the route plan will be given to all suppliers and sub-contractors to ensure drivers are aware of the designated route. This will be supplemented by on-site briefings which will further enhance this understanding.

Ecology Mitigation Measures

- 7.7 In response to consultation comments from MSDC's Ecology Consultant, a separate Ecology Statement for Parcel 1.7A and the construction compound has been carried out by an Ecologist, this is included as **Appendix F**.
- 7.8 The Ecology Statement demonstrates Parcel 1.7A has limited suitability for supporting protected species of bats, reptiles, hazel dormouse, nesting birds, amphibians or badgers due to the limited habitats and fencing reducing the likelihood of species using the Parcel. Much of Parcel 1.7A is bare ground with rubble piles and archaeology scars and small patches of unimproved grassland. The construction compound site has limited suitability to support protected species due to the volume of bare ground and the historical works that have taken place on the compound site.
- 7.9 The proposed areas of pre-commencement works will not impact the rest of the Phase 1C wider site and appropriate mitigation will be implemented though the wider site due to the habitat and protected species potentially present.
- 7.10 During construction, fuel spillages, run off and other potential pollution incidents have the potential to impact on adjacent habitats including the ponds and watercourses. The Principal Contractor will therefore ensure that appropriate equipment such as spill kits containing absorbent material will be available to site operatives. The Principal Contractor will train site operatives in the use of these spill kits. All reagents and chemicals will be clearly signed and appropriately stored, contained and banded.
- 7.11 Whilst Parcel 1.7A and the construction compound are unlikely to support bats, lighting levels and colour temperature will be considered in the design to avoid and reduce potential harm.
- 7.12 The Principal Contractor will adopt appropriate biosecurity measures to mitigate the risk of spreading invasive species (e.g. Himalayan balsam recorded within the Site adjoining watercourses).
- 7.13 Furthermore, the following best practice measures related to (but not limited to) the control of noise, dust and pollution will benefit the protection of habitats adjacent to the Site:
- All vehicles and mechanical plant will be fitted with exhaust silencers;
 - Acoustic covers used over generators and other plant;
 - Plant and machinery will be turned off when not in use;
 - Enclosure and sheeting of material stockpiles;
 - Sheltered location for material storage where appropriate;
 - The use of wheel washes to reduce the trafficking of soil onto adjacent highways with prompt clearance as a remedial action;

- The use of a bowser on-site during extended periods of dry weather to damp down dust;
- Sheeting of vehicles carrying spoil;
- Dust suppression measures for any on-site crushers; and
- Bunding of fuel stores and material stockpiles to prevent pollution.

Landscape and Visual Mitigation Measures

7.14 The Principal Contractor will ensure implementation to protect retained vegetation, limit the visual perception of the construction phase within the Site through considerate and appropriate topsoil and stockpile storage heights and keep the Site in a tidy condition, in line with the best practice methods.

Mitigation will include:

- Ensuring soil structures are protected where land would be used temporarily; and
- Restricting buildings within the main contractor compound, to two storeys in height.

Dust and Air Pollution Mitigation Measures

7.15 The Principal Contractor will be required to manage dust, air pollution, odour and exhaust emissions during the construction works in accordance with Best Practicable Means (BPM). Demolition and construction dust is expected to only represent a nuisance to exposed human receptors in immediate proximity to the construction area of the Site.

7.16 When required, dust suppression will be applied to the roads. In addition, construction dust will be controlled through the following measures, including (but not limited to):

- Demolition and Site Clearance:
 - Soft strip inside buildings before any dismantling and clearing the Site;
 - Ensure effective water suppression is used during deconstruction operations;
 - Avoid blasting techniques, using appropriate manual or mechanical alternatives; and
 - Bag and remove any biological debris or damp down such material.
- Earthworks:
 - Avoid scabbling (i.e. a mechanical process of removing a thin layer of concrete from a structure,
 - Typically achieved by compressed air powered machines) if possible;
 - Re-vegetate earthworks and exposed areas/soil stockpiles to stabilise surfaces as soon as practicable;
 - Use Hessian, mulches or tackifiers where it is not possible to re-vegetate or cover with topsoil, as soon as practicable; and

- Only remove the cover in small areas during work and not all at once.
- Construction:
 - Avoid scrubbling (roughening of concrete surfaces) if possible;
 - Ensure sand and other aggregates are stored in bunded areas and are not allowed to dry out, unless this is required for a particular process, in which case ensure that appropriate additional control measures are in place;
 - Ensure bulk cement and other fine powder materials are delivered in enclosed tankers and stored silos with suitable emission control systems to prevent escape of material and overfilling during delivery; and
 - For smaller supplies of fine powder materials ensure bags are sealed after use and stored to prevent dust.

Noise and Vibration Mitigation and Monitoring

- 7.17 The Principal Contractor will apply Best Practice Measures (as defined by section 72 of the Control of Pollution Act 1974 (Ref. 4)) to minimise construction noise and vibration on neighbouring sensitive receptors.
- 7.18 The recommendations of BS 5228: Code of practice for noise and vibration control on construction and open sites parts 1 and 2 (Ref. 5), will be implemented.
- 7.19 Regular meetings will be held with the clients at which noise can be discussed. All mitigation measures will be employed including the programming of the works. Plant will be requested as electric or super-silenced diesel as practicable. If necessary, plant will be screened.

Water Quality and Pollution Management

- 7.20 The Principal Contractor will manage site activities and working methods to protect the quality of surface water and groundwater resources. Precautions will also be taken to prevent damage to services and to avoid pollution during ground penetration, excavation and service diversions.
- 7.21 Hill Group have a specific reporting procedure in place of any pollution incidents on their internal hub, therefore any incident will be logged and dealt with on an individual case-by-case basis.
- 7.22 Monitoring systems and emergency procedures in the case of any pollution incidents will be employed during the construction works. Best Practice Measures (BPM) will be used (e.g. through the use of silt traps and the re-use of water in wheel washers) where appropriate. The measures to be implemented are:

- Sediment in run off:
 - The use of water-assisted dust sweepers on the access and local roads will be used to suppress dust and remove any material tracked out of the Site as necessary;
 - Site access points will be regularly cleaned to prevent build-up of dust and mud; and
 - Earth movement will be controlled to reduce the risk of construction silt combining with the Site surface water runoff.
- Leaks and spillages:
 - Spillages and leakages will be immediately contained in line with an Emergency Response Plan (ERP) and managed through the use of geotextile bunding of adequate capacity (110%), to isolate and minimise the ingress of surface water runoff to non-decommissioned boreholes or exposed surface water drainage pipes. Valves and trigger guns will be protected from vandalism and kept locked when not in use;
 - An emergency spillage action plan will be produced, which Site staff will have read and understood. On-site provisions will be made to contain a serious spill or leak through the use of booms, bunding and absorbent material;
 - Wherever possible, plant and machinery will be kept away from the drainage system and will have drip trays beneath oil tanks / engines / gearboxes / hydraulics, which will be checked and emptied regularly via a licensed waste disposal operator;
 - Following the discharge of surface water run-off and de-watering effluents to settling tanks, the drainage would be routed to oil interceptors prior to discharge to sewer;
 - Where appropriate, the majority of concrete used will be pre-mixed and delivered from an off-site source, thereby negating the need to mix concrete on-site and reducing the creation of alkaline wastewater. Any mixing and handling of wet concrete on-site will be undertaken in designated impermeable areas, away from any drainage channels or surface water;
 - A designated impermeable area will be used for any washing down or equipment cleaning associated with concrete or cementing processes and wastewater will be discharged to the foul drainage system (with approval from Southern Water) or contained and removed by tanker to a suitable discharge location by a suitably licenced waste operator; and
 - The proposed drainage / service runs will be surrounded by appropriate granular bedding materials and located above the static level of any shallow groundwater. The drainage network installed as part of the Proposed Development will be constructed to meet with Building Regulations 2010, Part H (Ref. 7).
- Groundwater Flow and Quality:
 - Pile casing will be used during piling and the area around the piling will be isolated from

- surface water until piling is complete;
 - If perched groundwater is encountered during establishment of basement and core foundations dewatering may be required;
 - In the event that ground contamination is discovered, work will stop immediately and measures will be taken to prevent disturbance and mobilisation of contaminants, until the contamination has been treated in-situ or removed for off-site disposal or treatment;
 - If contaminated soils are encountered at the position where piling is due to be undertaken, then these materials should be removed prior to piling in order to prevent the dragging of contaminated soils with the piles to depth;
 - Contaminated soil requiring disposal will be excavated and kept separate from other soil and waste materials in protected temporary stockpiles prior to disposal;
 - Water arising from excavations will be disposed of to the local sewer network (subject to agreement with Thames Water) if uncontaminated and following the removal of silt via silt buster or other settlement technology;
 - Damp-proof membranes will be incorporated into the construction. These membranes will prevent the ingress of groundwater and reduce the risk of contaminants from reaching underground strata or groundwater. The watertight basement will therefore prevent any interior leaks or spillages from freely percolating into the shallow groundwater.
- Preventing an increase in flood risk during construction:
 - Topsoil and other construction materials will be stored outside of the 1 in 100 year floodplain extent. If areas located within Flood Zone 2 are to be utilised for the storage of construction materials, then a permit will be obtained from the Environment Agency;
 - Connectivity will be maintained between the floodplain and the adjacent watercourses, with no changes in ground levels within the floodplain as far as practicable; and
 - The construction laydown area site office and supervisor will be notified of any potential flood occurring by use of the Floodline Warnings Direct service.
- Minimising drainage system disturbance:
 - All existing utilities will be identified and marked as far as practicable prior to works commencing;
 - Signs will be used to warn of the presence of any drainage systems; and
 - Any damage to existing drainage networks will be immediately repaired.
- Monitoring:
 - Seepage analysis and groundwater level monitoring will be carried out as appropriate to assess deformation and stability of surrounding structures and properties as necessary.
 - If monitoring demonstrates unsatisfactory levels of solids or other pollutants in surface

water discharged from the Site, measures will be implemented to control suspended solids or other polluted discharge to watercourses (e.g. changes to Site drainage and settlement facilities and / or use of flocculants (substances which promote the clumping of particles)).

Waste Management

7.23 Waste will be generated at all stages of construction works. All waste will be managed and monitored in accordance with an appropriate site waste management plan. The following measures will be implemented:

- Waste reduction commitment;
- Subcontractors required to document actions which have been taken relating to waste;
- Use waste disposal businesses that diverts a large percentage of waste they receive away from landfill;
- Energy usage on site will be recorded and monitored;
- Document the amount of waste expected and generated; and
- Development of a site waste management plan.

Re-use of Material On-site

7.24 Where possible, material that is generated through the construction process will be re-used on site. This will help in reducing vehicle movements that will be delivering new materials, therefore helping to reduce costs and environmental impacts.

Smart Procurement

7.25 All measures will be undertaken during the procurement stage to ensure that the impact of the works is minimised. Contractors will be partially selected upon their use of local staff who can travel to the site via public transport, walking or cycling. Suppliers within the local supply chain will also be used wherever possible to minimise the distance travelled by vehicles delivering materials to the site.

Sustainable Travel Information for Staff

7.26 There will be a considerable number of journeys to and from the proposed development made by the construction site staff. The nature of the numbers and timings of staff arrivals will vary during by phase during the construction phases, however it is anticipated that the majority arrivals would occur before the AM peak and departures before the PM peak.

7.27 All construction site staff will be made aware of the sustainable travel options to and from the site, and be informed of any site-specific travel information during induction training.

- 7.28 Safe and secure cycle parking will be provided within the site for any construction staff or visitors wishing to cycle to the site.

Compliant Safe Urban Driving Course

- 7.29 A requirement for all drivers to take a compliant Safe Urban Driving Course will be considered to ensure the safety of vulnerable users such as cyclists, pedestrians and motorcyclists. The training should be fully aligned to meet the requirements of FORs and CLOCs standards.

8 IMPLEMENTATION, MONITORING AND UPDATING

Logistics Manager / Banksman

- 8.1 The principal contractor will appoint a member of staff for the day-to-day organisation and monitoring of the CEMP for Parcel 1.7A and the construction compound. This includes the implementation and management of the CEMP for the lifetime of the construction project.
- 8.2 A member of staff will also be responsible for liaison with local residents, businesses and groups and will be required to collect the following information throughout the construction process:
- Number of vehicle movements to site
 - Total
 - Vehicle size, type and age
 - Time spent on site
 - Consolidation usage (if appropriate)
 - Origin and destination of vehicle
 - Deliver/ collection accuracy compared to schedule
 - Breaches and complaints
 - Community concerns about construction activities
 - Vehicle routing
 - Unacceptable queuing and parking
 - Adherence to safety and environmental standards and programmes
 - LEZ and ULEZ compliance
 - Anti-idling
 - Safety
 - Logistics related incidents
 - Record of associated fatalities and series injuries
 - Methods staff are travelling to site
 - Vehicles and operators not meeting safety requirements
 - Personal safety surrounding the site
 - Description of the contractor's handbook
 - Description of driver's handbook
- 8.3 The collected data will be utilised to inform the ongoing implementation of this CEMP and minimise the impact of the associated construction works on the local highway network and neighbouring communities.
- 8.4 Where possible, no construction related equipment, structures or activities will be undertaken on or over the public highway. Should such activities occur authorisation should be sought beforehand.

Compliance

- 8.5 Contracts with suppliers and sub-contractors will be managed to ensure that all third parties associated with the works adhere to all standards set out. Monitoring and review of construction activity to the site will be the responsibility of the contractor, who will monitor and report performance.

Appendix A

<https://eur02.safelinks.protection.outlook.com/?url=http%3A%2F%2Fwww.midsussex.gov.uk%2F&data=05%7C02%7CJoseph.Swift%40midsussex.gov.uk%7C5d7ae5dee4df430f621908df0384351a%7C248de4f9d13548cca4c8babd7e9e8703%7C0%7C0%7C639233538499121725%7CUnknown%7CTWFPfbGZsb3d8eyJFbXB0eU1hcGkiOnRydWUsIlYiOiIwLjAuMDAwMCIiIAoiXjAw4zMiIsIkFOljoiTWFpbClldUIjoyfQ%3D%3D%7C0%7C%7C%7C&sdata=jrkoJwsSnMagbw1%2FckiPz1k8O8oRowlqu9CuScvqbhs%3D&reserved=0>

“Working together for a better Mid Sussex”

-----Original Message-----

From: mpc@midsussex.gov.uk <mpc@midsussex.gov.uk>

Sent: 26 August 2026 12:12

To: Oliver Benson <oliver.benson@midsussex.gov.uk>

Subject: Service request - SR/26/3533 Burgess Hill Northern Arc, Land N And NW Of Burgess Hill, Between Bedelands Nature, Reserve In The East And, Goddard's Green Waste Water Treatment Works In The West, ,

Oliver Benson

This is sent from an unmonitored address, please do not respond.

Please see attached Service Request

SR/26/3533

Type: Planning - consultation.

Details: Planning application consultation for application - DM/26/2064 - Burgess Hill Northern Arc, Land N And NW Of Burgess Hill, Between Bedelands Nature Reserve In The East And, Goddard's Green Waste Water Treatment Works In The West

Discharge of Condition 8 (CEMP) in relation to planning application

DM/21/3279 in respect of reserved matters area DM/25/1986 (Phase 1C) We would be grateful for your comments by 16th September 2026

Regards

Communities Support Team

Mid Sussex District Council

WEST SUSSEX COUNTY COUNCIL CONSULTATION

TO:	Mid Sussex District Council FAO: Joseph Swift
FROM:	Stephen Gee WSCC – Highways Authority
DATE:	2 September 2026
LOCATION:	Burgess Hill Northern Arc, Land N And NW Of Burgess Hill, Between Bedelands Nature Reserve In The East And, Goddard's Green Waste Water Treatment Works In The West
SUBJECT:	DM/26/2064 Discharge of Condition 8 (CEMP) in relation to planning application DM/21/3279 in respect of reserved matters area DM/25/1986 (Phase 1C).
DATE OF SITE VISIT:	n/a
RECOMMENDATION:	More Information

The CEMP relates to Phase 1C of the Brookleigh development.

A maximum of 25-30 HGV deliveries would be made each day and HGVs would access the site via Issacs Lane and the A273, A2300.

An average of 80-100 subcontractors vehicles could be on site each day. Parking provision within the compound is limited to 24 vehicles and the CEMP identifies in 5.13 that *"Parking in other areas of the site development, apart from those signed as being for car parking (which will be located within the compound area), such as on the site access roads will not be permitted."*

Confirmation should be provided on the accuracy of the number of subcontractors and if correct additional parking provision should be identified within the site for the period the demand exists, without this it is likely subcontractors will park along Holmbush Avenue or adjoining development plots, rather than park within town centre car parks as the CEMP suggests and utilise the bus service to access the site.

Wheel washing facilities are to be provided on site, however no locations are shown. Road sweeping will be undertaken as and when required.

Conclusion

Confirmation should be provided on the number of subcontractors and additional parking provision identified.

Confirmation should be provided on the location of wheel washing facilities.

Stephen Gee
West Sussex County Council – Planning Services

Lauren Wright

From: Joseph Swift <Joseph.Swift@midsussex.gov.uk>
Sent: 14 September 2026 10:38
To: Luke Ince-Green
Cc: Louise Yandell; Oliver Mealey
Subject: DM/26/2064
Attachments: Response_21730.pdf



Good morning Luke,

RE: Discharge of Condition 8 (CEMP) in relation to planning application DM/23/0747 in respect of reserved matters area DM/25/1986 (Phase 1C)

AT: Burgess Hill Northern Arc, Land N And NW Of Burgess Hill, Between Bedelands Nature Reserve In The East And, Goddard's Green Waste Water Treatment Works In The West

REFERENCE: DM/26/2064

Please see attached a copy of the Ecology consultants comments.

As you can see from these comments additional ecology information is required in order to satisfy this condition.

It is noted from previous correspondence that a number of the surveys are to follow. I've not checked with the Ecology Consultant, but it could be possible to discharge this condition in relation to individual parcels, particularly if there are certain parcels that do not require any further survey works to be carried out. Happy to have a meeting to discuss if that would be beneficial.

Many thanks

Joseph Swift BA (Hons) MPLAN
Senior Planning Officer (Brookleigh)
01444 477319
Mid Sussex District Council
joseph.swift@midsussex.gov.uk
www.midsussex.gov.uk



Working together for a better Mid Sussex

The information contained in this email may be subject to public disclosure under the Freedom of Information Act 2000. Unless the information contained in this email is legally exempt from disclosure, we cannot guarantee that we will not provide the whole or part of this email to a third party making a request for information about the subject matter of this email. This email and any attachments may contain confidential information and is intended only to be seen and used by the

named addressees. If you are not the named addressee, any use, disclosure, copying, alteration or forwarding of this email and its attachments is unauthorised. If you have received this email in error please notify the sender immediately by email or by calling +44 (0) 1444 458 166 and remove this email and its attachments from your system. The views expressed within this email and any attachments are not necessarily the views or policies of Mid Sussex District Council. We have taken precautions to minimise the risk of transmitting software viruses, but we advise you to carry out your own virus checks before accessing this email and any attachments. Except where required by law, we shall not be responsible for any damage, loss or liability of any kind suffered in connection with this email and any attachments, or which may result from reliance on the contents of this email and any attachments.



Date: 11 September 2026
Our ref: 21730

Joseph Swift
Mid Sussex District Council
Oaklands Road
Haywards Heath
West Sussex
RH16 1SS

By email only: planninginfo@midsussex.gov.uk

Thank you for requesting advice on this discharge of condition from Place Services' ecological advice service. This service provides advice to planning officers to inform Mid Sussex District Council planning decisions with regard to potential ecological impacts from development.

Application:	DM/26/2064
Location:	Burgess Hill Northern Arc, Land N And NW Of Burgess Hill, Between Bedelands Nature Reserve In The East And, Goddard's Green Waste Water Treatment Works In The West
Proposal:	Discharge of Condition 8 (CEMP) in relation to planning application DM/21/3279 in respect of reserved matters area DM/25/1986 (Phase 1C)

Thank you for consulting Place Services on the above discharge of Condition application.

Condition

Condition 8. Prior to the commencement of development within each reserved matters area, a Construction Environmental Management Plan (CEMP) shall be submitted to and approved in writing by the Local Planning Authority in respect of development within that reserved matters area. The CEMP shall include amongst other matters details of:

- o The appropriate Mitigation Measures stated as being contained within the CEMP in Table 16-1

'Summary of Mitigation Measures from within the Technical ES Chapters', Chapter 16 Mitigation Register, of the Environmental Statement Volume 1 (December 2018).

- o setting out avoidance and mitigation measures in respect of wildlife and habitats;
- o a timetable for the commencement, construction, occupation and completion of the development;
- o the anticipated number, frequency and types of vehicles used during construction
- o the method of access and routing of vehicles during construction and directional signage for the purposes of such
- o the siting and layout of site compounds and welfare facilities for construction workers
- o the provision of parking of vehicles by site operatives and visitors
- o the provision for the loading and unloading of plant, materials and removal of waste
- o the provision for the storage of plant and materials used in construction of the development
- o the design, erection and maintenance of security hoardings and other measures related to site health and safety
- o hours of construction working;
- o details of construction lighting;
- o measures to monitor and control noise and vibration affecting nearby residents;
- o the provision of wheel washing facilities and other works required to mitigate the impact of construction upon the public highway, including the provision of temporary Traffic Regulation Orders;
- o dust control measures;
- o pollution incident control and site contact details in case of complaints;
- o a scheme for community liaison and public engagement during construction, including the provision of information to occupiers moving onto the site before the development is complete
- o contact details of site operations manager, contracts manager, and any other relevant personnel.

The CEMP shall be in accordance with the Ecological Impact Assessment Section 73 Application - Incursions to Ancient Woodland (AECOM Limited, April 2022)

The construction works within that reserved matters area shall thereafter be carried out at all times in accordance with the approved Construction Environmental Management Plan, unless any variations are otherwise first submitted to and approved in writing by the Local Planning Authority.

Reason: To protect the local landscape, biodiversity within the site, the local environment and neighbouring residential amenity and to accord with Policies DP9, DP26 and DP38 of the Mid Sussex District Plan.

Comments

We have reviewed the Construction Environmental Management Plan (Hill Group Ltd, September 2026) which has been submitted in order to discharge Condition 8.

The submitted Construction Environmental Management Plan (CEMP) provides generic ecological measures, which are not considered sufficiently robust to demonstrate protection of irreplaceable habitat, protected and Priority species / habitats.

We recommend that applicant corresponds with their Suitably Qualified Ecologist who is providing information to meet the requirements of Condition 20 of DM/23/0747 to include detailed ecological mitigation measures within this CEMP.

Recommendation

We are unable to recommend the discharge of Condition 8 at an ecological perspective until the additional information outlined above has been provided.

Please do not hesitate to contact us if you have any queries in relation to this advice.

Yours sincerely,

Hamish Jackson ACIEEM BSc (Hons)

Senior Ecological Consultant

Place Services at Essex County Council



Place Services provide ecological advice on behalf of Mid Sussex District Council.

Please note:

This letter is advisory and should only be considered as the opinion formed by specialist staff in relation to this particular matter.

We are unable to respond directly to applicants/agents or other interested parties. Any additional information, queries or comments on this advice that the applicant/agent or other interested parties may have, must be directed to the Planning Officer at the relevant LPA, who will seek further advice from us where appropriate.

Place Services have a policy relating to the use of AI. Unless otherwise stipulated, any AI use will be limited to basic proof-reading, grammar, and spelling correction. This response has been reviewed by the author(s). If you have any queries, please [contact us](#) for information about our AI guidance.

Appendix B

Notes:

All contractors must visit the site and be responsible for taking and checking Dimensions.

All construction information should be taken from figured dimensions only.

Any discrepancies between drawings, specifications and site conditions must be brought to the attention of the supervising officer.

This drawing and the works depicted are the copyright of JTP.

This drawing is for planning purposes only. It is not intended to be used for construction purposes. Whilst all reasonable efforts are used to ensure drawings are accurate, JTP accept no responsibility or liability for any reliance placed on, or use made of, this plan by anyone for purposes other than those stated above.



P02	12.01.26	Post planning revisions following Urban Design Officer comments received	AN	ABL
P01	30.07.25	Planning Submission	ABL/RAP	DEC
Rev	Date	Description	Drawn	Chkd

Drawing Status
PLANNING

Client
Hill Holdings




Project
**Ph1c Northern Arc
Burgess Hill**

Drawing Title
**Proposed Illustrative
Masterplan**

Scale @ A1 1:1000 Job Ref. 02119

Drawing No. 02119_ MP10 Revision P02

Scale Bar 0 10 20 30 40 50m



Appendix C

KEY

- 10 Plot Parking Space
- UC Unallocated Communal Parking
- V Visitor Parking Space
- U Unallocated Parking
- R Retail / School Drop Off Parking
- EC Extra Care Parking
- CC Car Club Parking
- SS Substation Parking
- EV Electric Vehicle Charging Point
- CS Cycle Storage
- BS Bin Storage
- BCP Bin Collection Point
- ASHP Air Source Heat Pump location

CLAGUE ARCHITECTS

www.clague.co.uk 01227 702 060 info@clague.co.uk

Client
Hill Residential

Project Title
Burgess Hill
Northern Arc
Phase 1C

Drawing Description
Site Layout Plan
Sheet 1 of 3


Scale	Date	Created	Checked
1:500 @ A1	May 2026	MTP	

Drawing Status


PRELIMINARY

Project - Originator - Function - Spatial - Form - Discipline - Number - Revision

NA1C -CLA- ZZZ - XX - D -A- 00001 P3

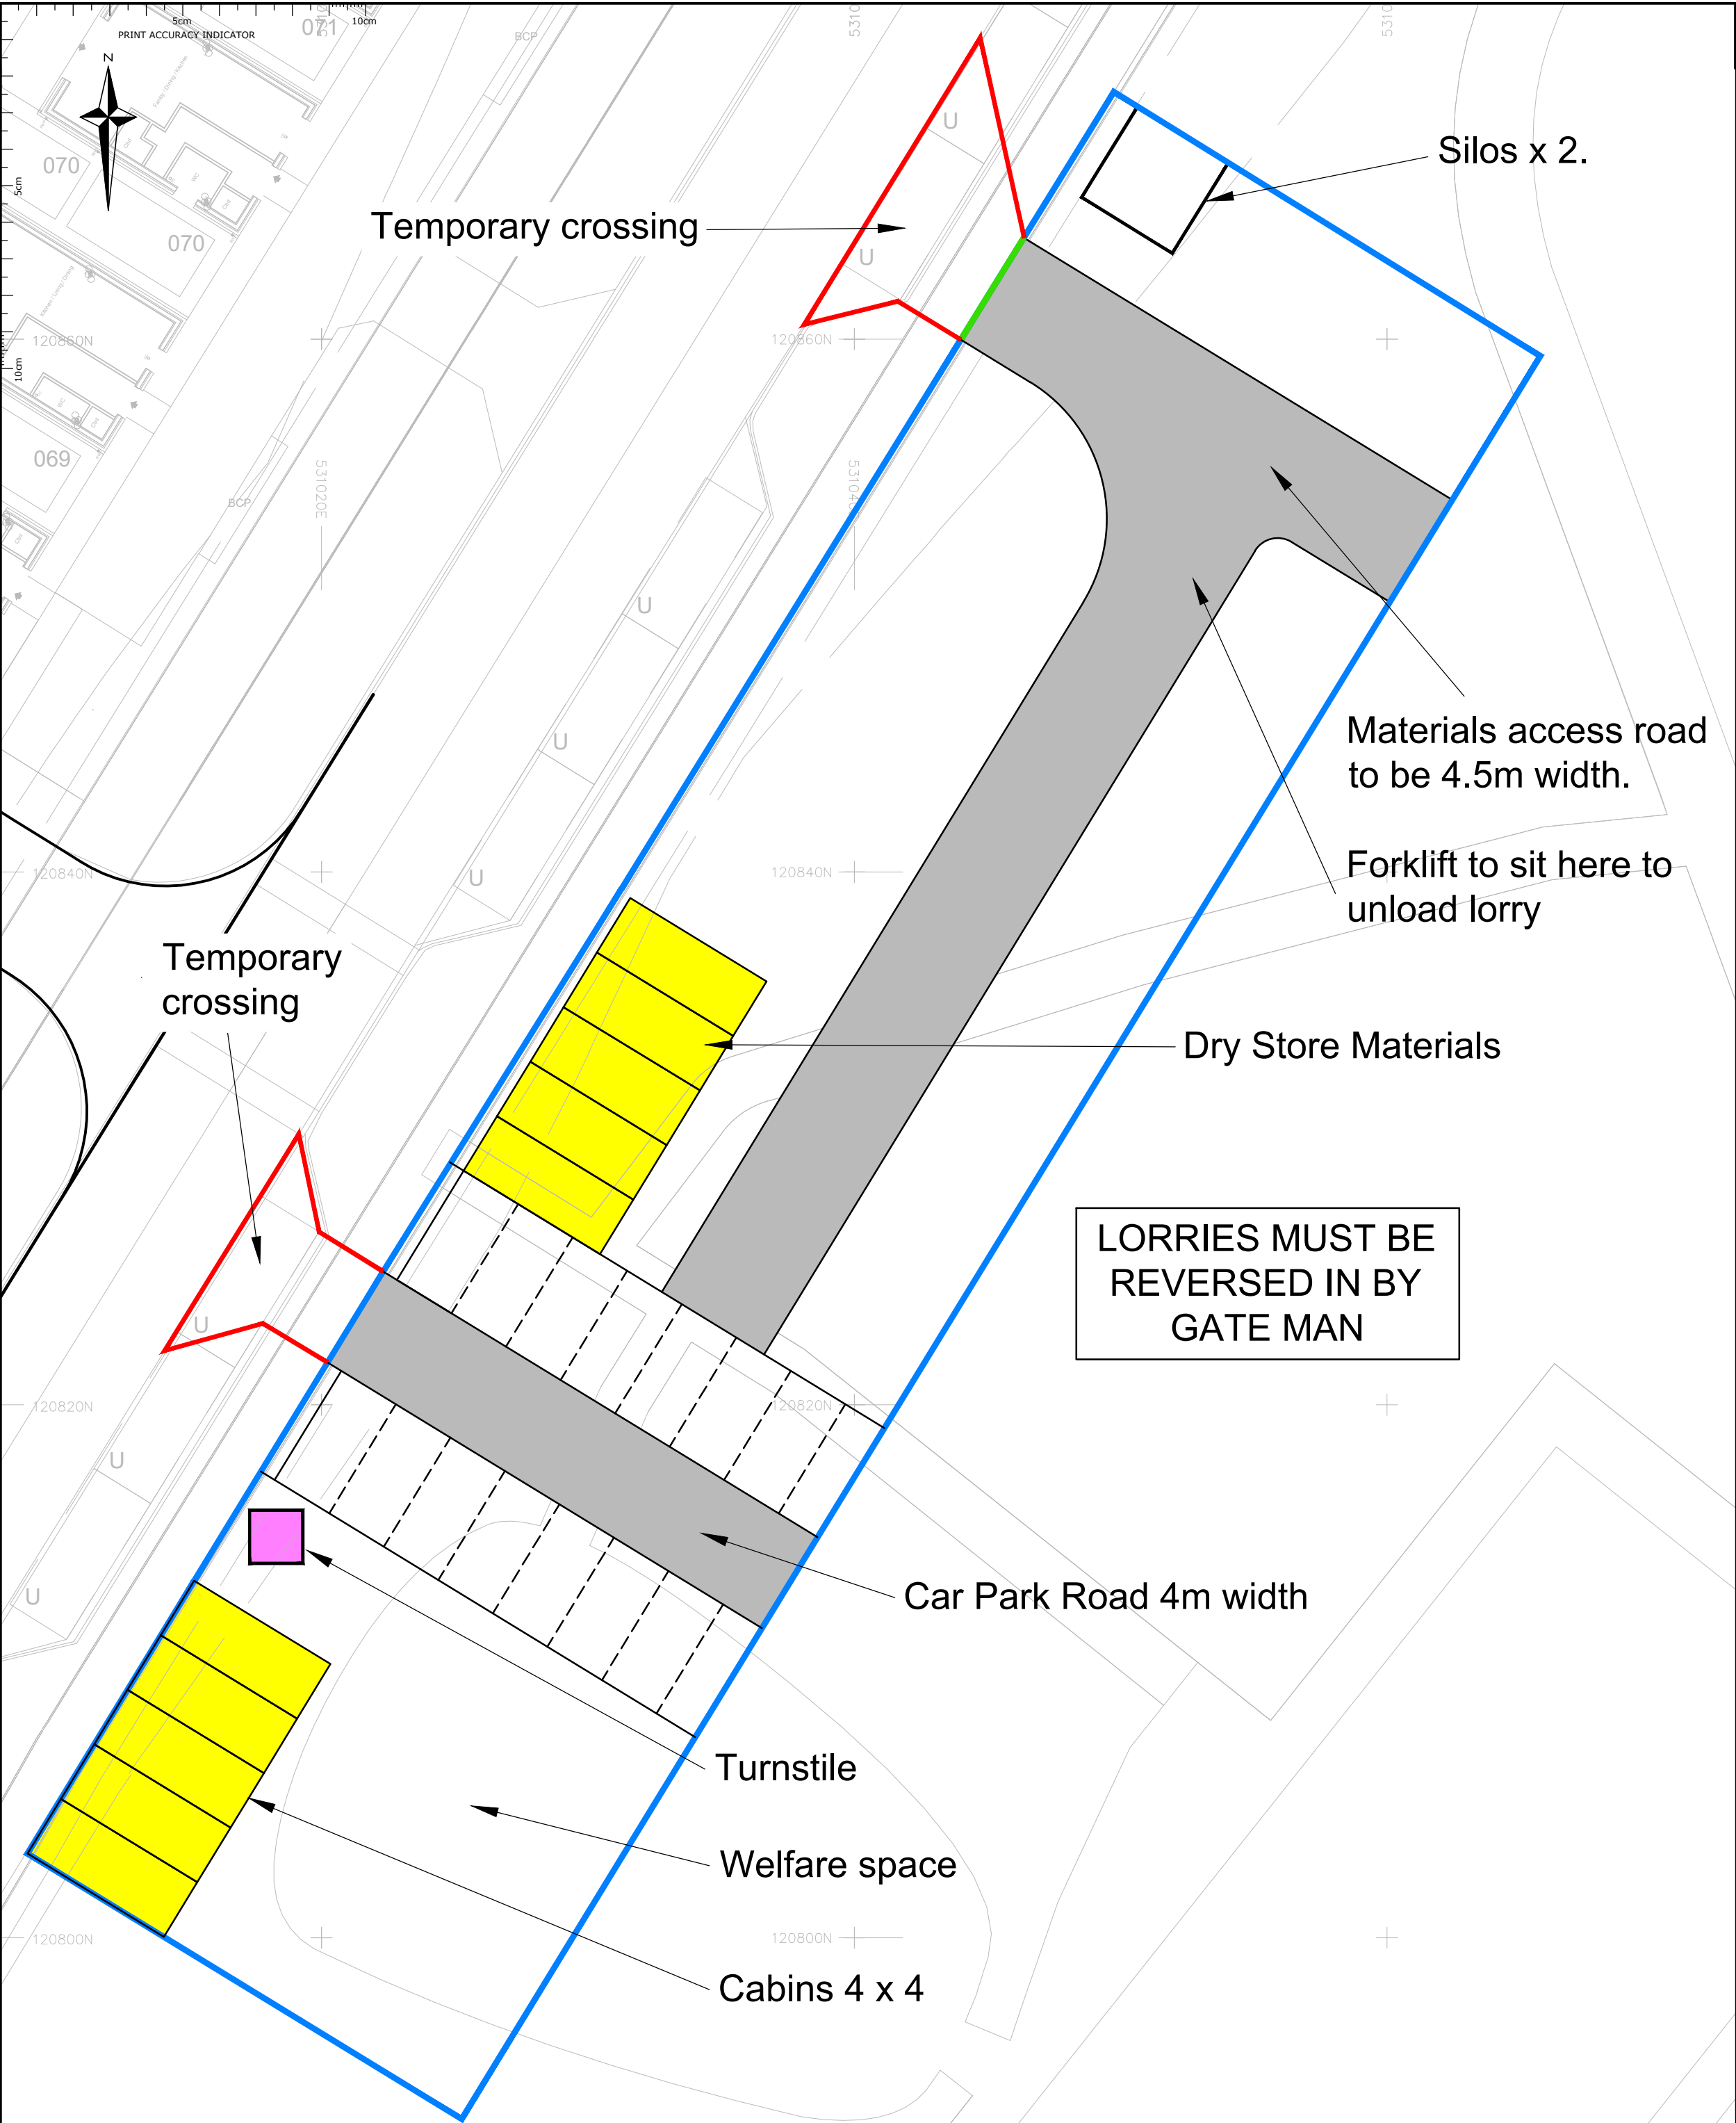

THIS DRAWING IS COPYRIGHT AND MUST NOT BE REPRODUCED IN WHOLE OR PART WITHOUT WRITTEN AUTHORITY

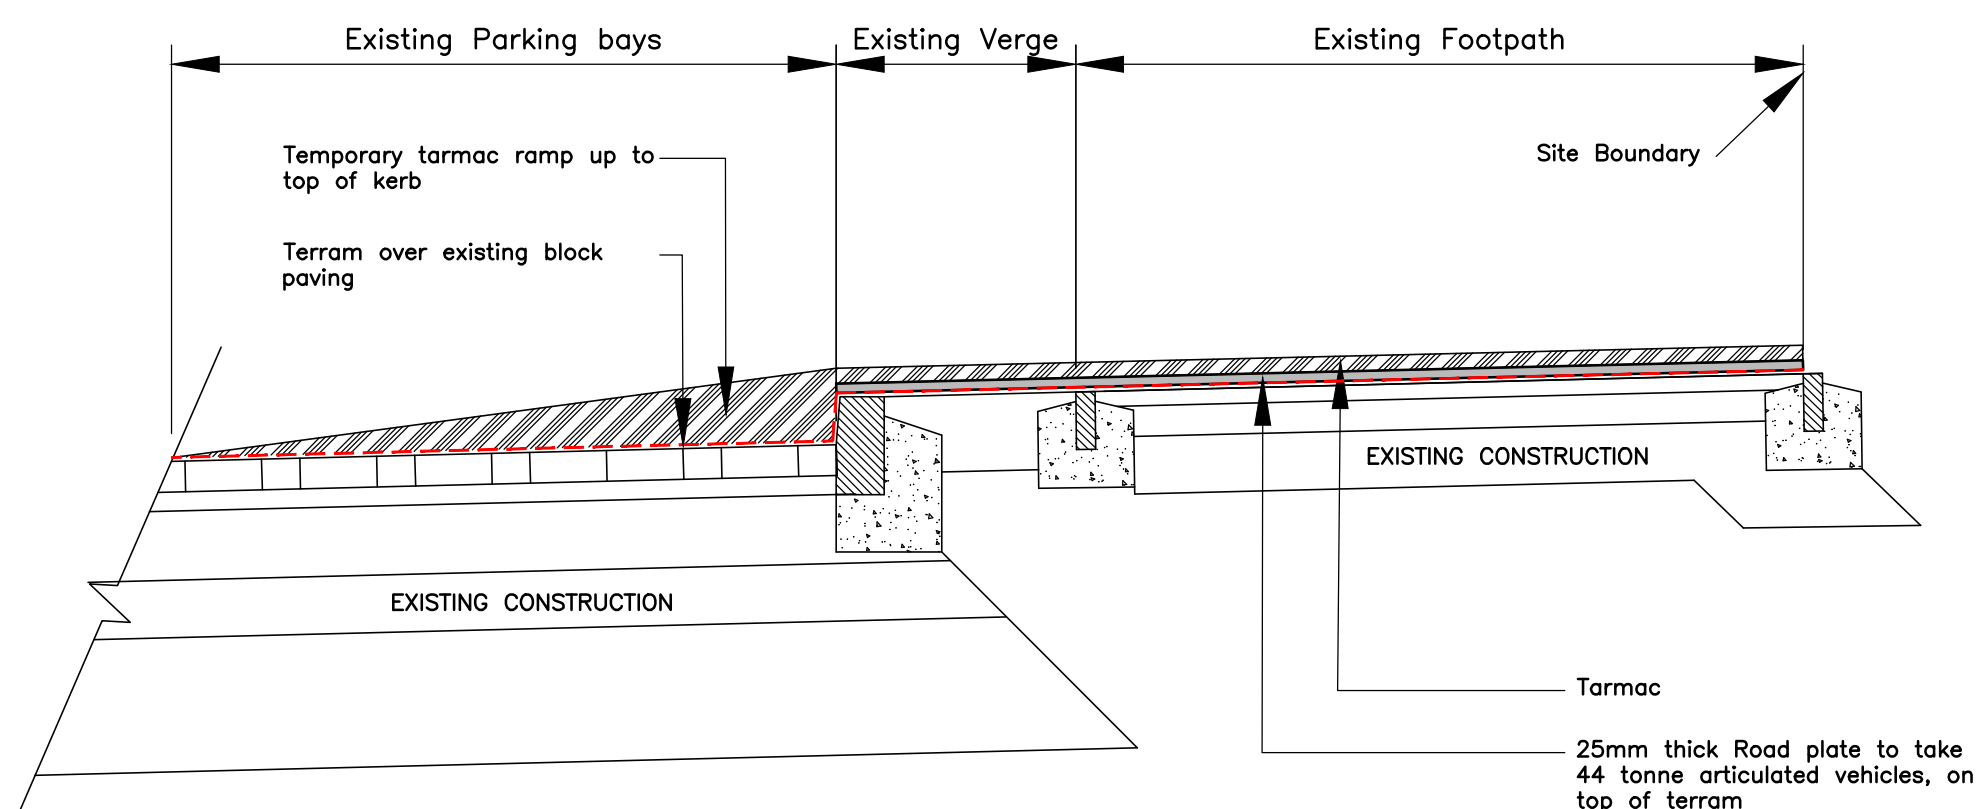

Typical Section Through New Temporary Access to Compound Area

Scale 1:20

PROJECT
Burgess Hill
Northern Arc
Phase 1C

CLIENT


DRAWING
Site Compound Layout

DATE 24/09/2026
SCALE (A2)- 1:200
DRAWN BY AB
CHECKED BY LRW


REV.	DATE	AMENDMENT	BY	CHKD

STATUS		INFORMATION	
WALKERS JOB NUMBER 7714		REV. P01	
DRG NO. NA1C-WAC-XXX-XX-D-C-10007		Walker Associates Consulting Limited Structural and Civil Engineers 13 Capricorn Centre Crane Farm Road Basilston, Essex SS14 3JL 01268 530 500 walker-associates.co.uk	


Appendix D

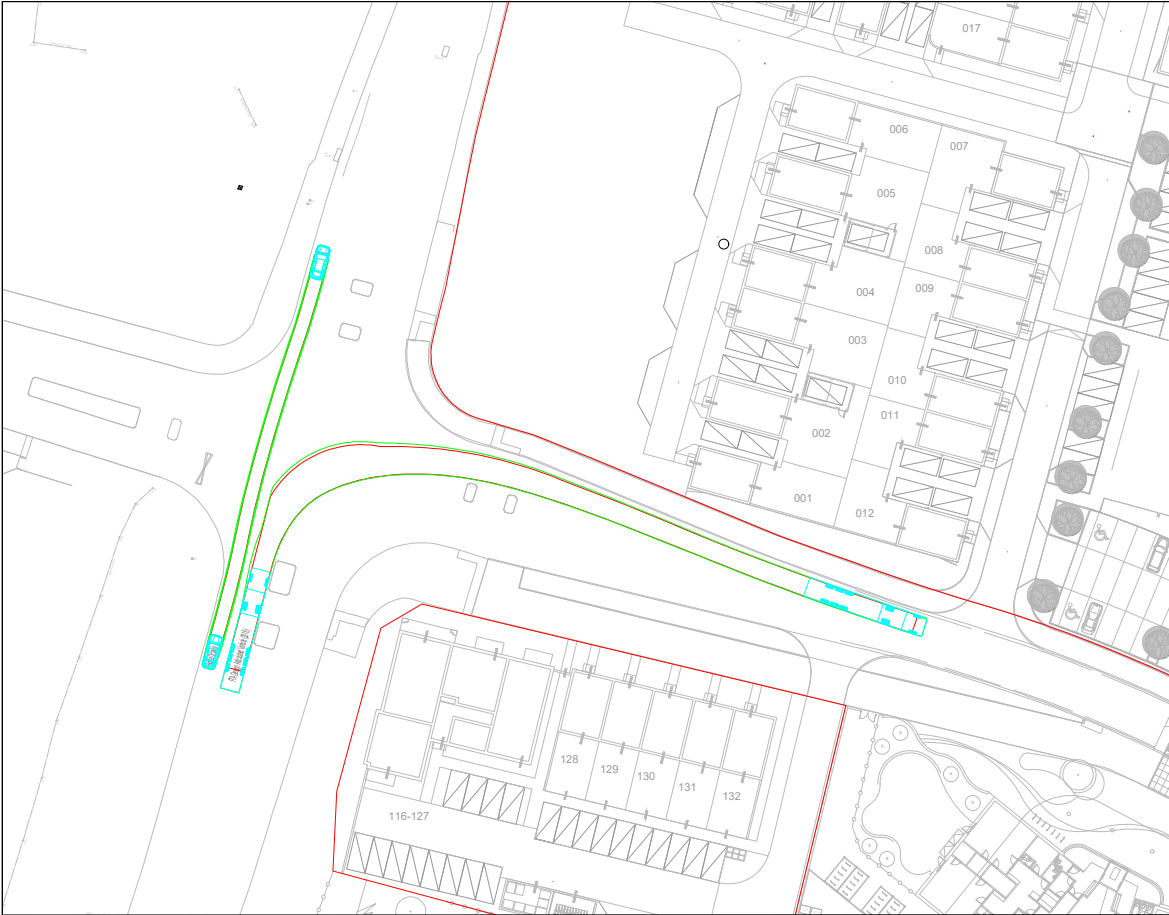


HGV TURNING RIGHT ACCESSING SITE

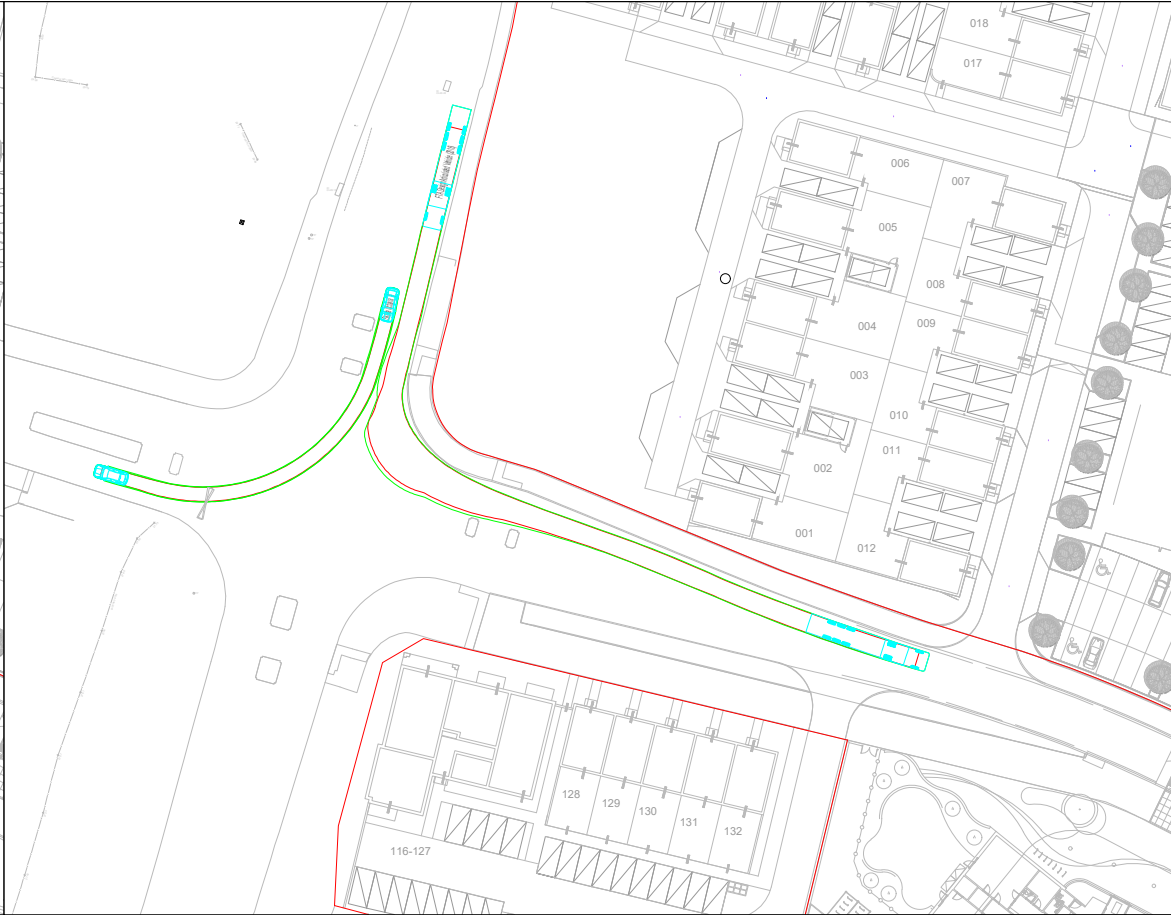

HGV TURNING LEFT ACCESSING SITE

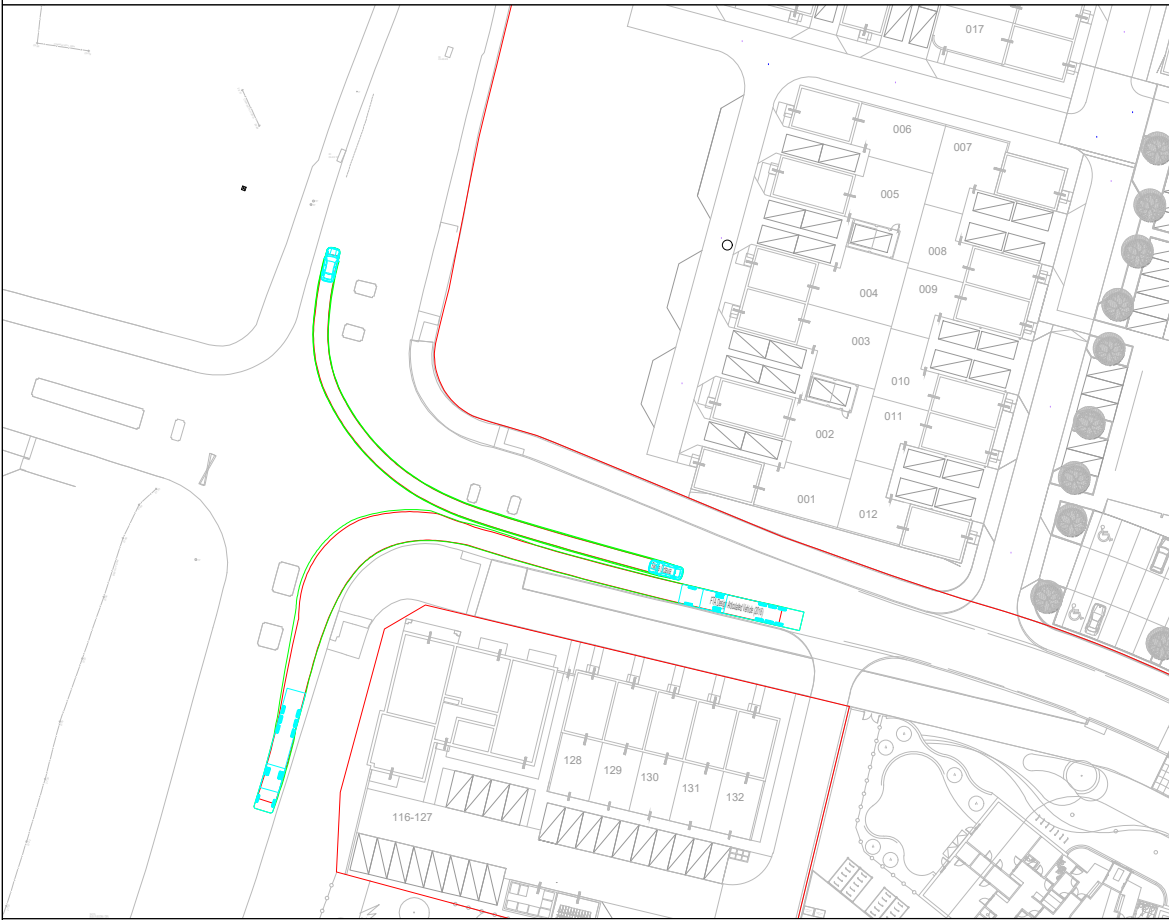

HGV TURNING LEFT EGRESSING SITE

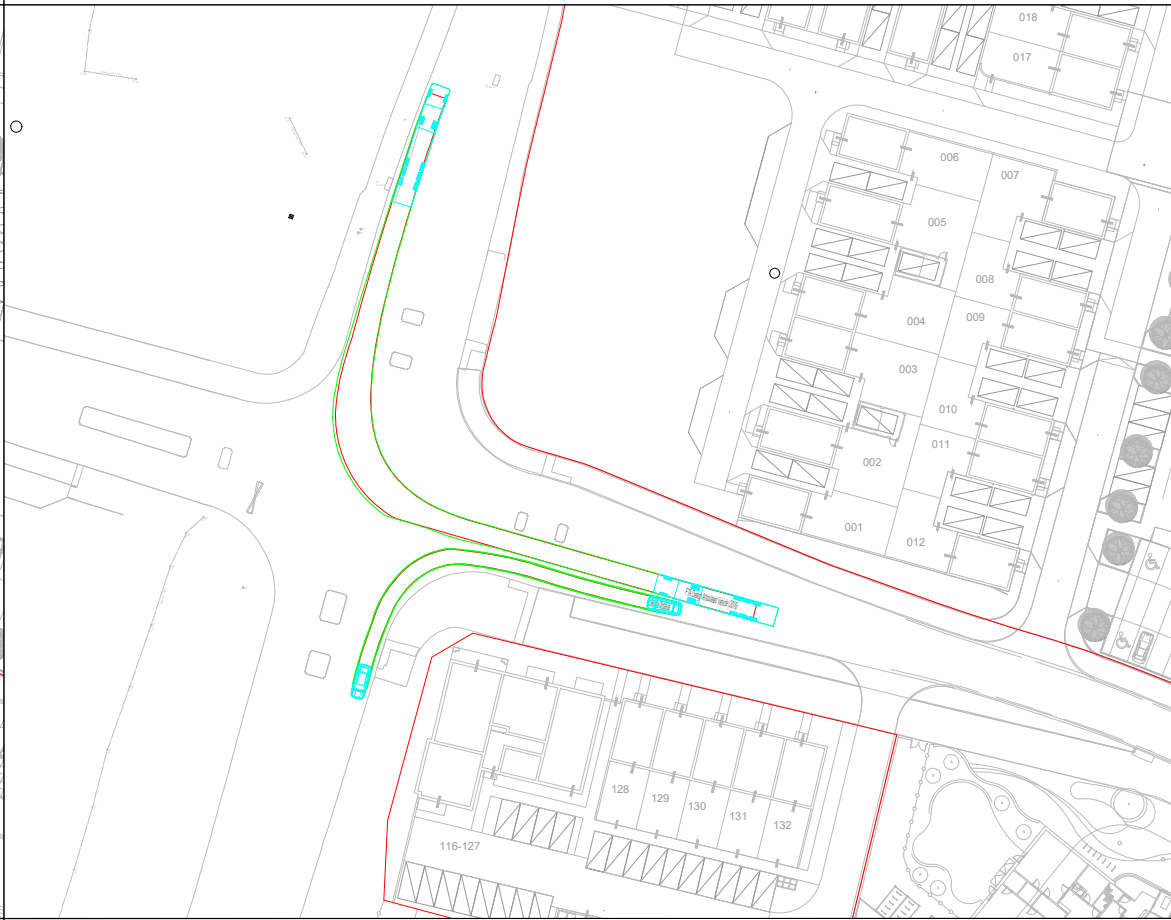

HGV TURNING RIGHT EGRESSING SITE

Project Name

PHASE 1C,
BURGESS HILL NORTHERN ARC

Project Phase

PRELIMINARY

Title

HGV VEHICLE TRACKING AT
SITE ACCESS

paulbasham

associates

Paul Basham Associates Ltd

The Lambourn, Wyndyke Furlong, Abingdon,

Oxfordshire, OX14 1UJ

01235 352150

info@paulbashamassociates.com www.paulbashamassociates.com

Client

Hill

The drawings, information and data recorded in this document ("the information") is the property of Paul Basham Associates. This document and the information are solely for the use of the authorised recipient and this document may not be used, copied or reproduced in whole or part for any purposes other than which it was supplied by Paul Basham Associates. Paul Basham Associates makes no representation, undertakes no duty and accepts no responsibilities to any third party who may use or rely upon this document or the information.

General notes

1. This drawing is intended to be read in conjunction with all relevant Architects, Engineers, Services and Specialist Drawings, Details and specifications.

2. Any variations or discrepancies between these drawings in terms of dimensions or details should be drawn to the attention of the Architect and/or the Engineer for clarification.

3. All figured dimensions to be taken in preference to scaled dimensions. Do not scale this drawing.

4. Paul Basham Associates accepts no responsibility for the accuracy of background information produced by third parties – this must be treated as indicative only. Third party plans are included as per the following:

4.1. Site Layout

5. This drawing should only be used for construction if the project phase in the title frame below is shown as "construction". Paul Basham Associates take no responsibility for construction works undertaken to drawings which are not marked under this phase.

KEY

PHASE 1C BURGESS HILL NORTHERN ARC
SITE BOUNDARY

VEHICLE PROFILE (NOT TO SCALE)

FTA Design Articulated Vehicle (2016)

Overall Length

Overall Width

Overall Body Height

Min Body Ground Clearance

Max Track Width

Lock to lock time

Kerb to Kerb Turning Radius

16.480m

2.550m

3.870m

0.515m

2.470m

3.00s

6.600m

Skoda Octavia

Overall Length

Overall Width

Overall Body Height

Min Body Ground Clearance

Max Track Width

Lock to lock time

Kerb to Kerb Turning Radius

4.572m

1.765m

1.488m

0.248m

1.713m

4.90s

5.100m

NORTH

PRELIMINARY

DRAWING/DESIGN IS STILL 'IN DEVELOPMENT'
YOU ARE ADVISED TO MAKE DUE ALLOWANCE

0m50m


1:1000

P01	FIRST ISSUE	08.07.26	LJW	JAM
Rev	Description	Date	By	App'd
Date Created	Drawn By	Approved By	Suitability Code	
08.07.26	LJW	JAM	-	
PBA Project Number		Scale	(AT A3)	
1041.0010		1:1000		
PBA Drawing No:				Revision
1041.0010-0001				P01

QMS2011/v9/020525/IDR

Appendix E

Burgess Hill Tender Programme

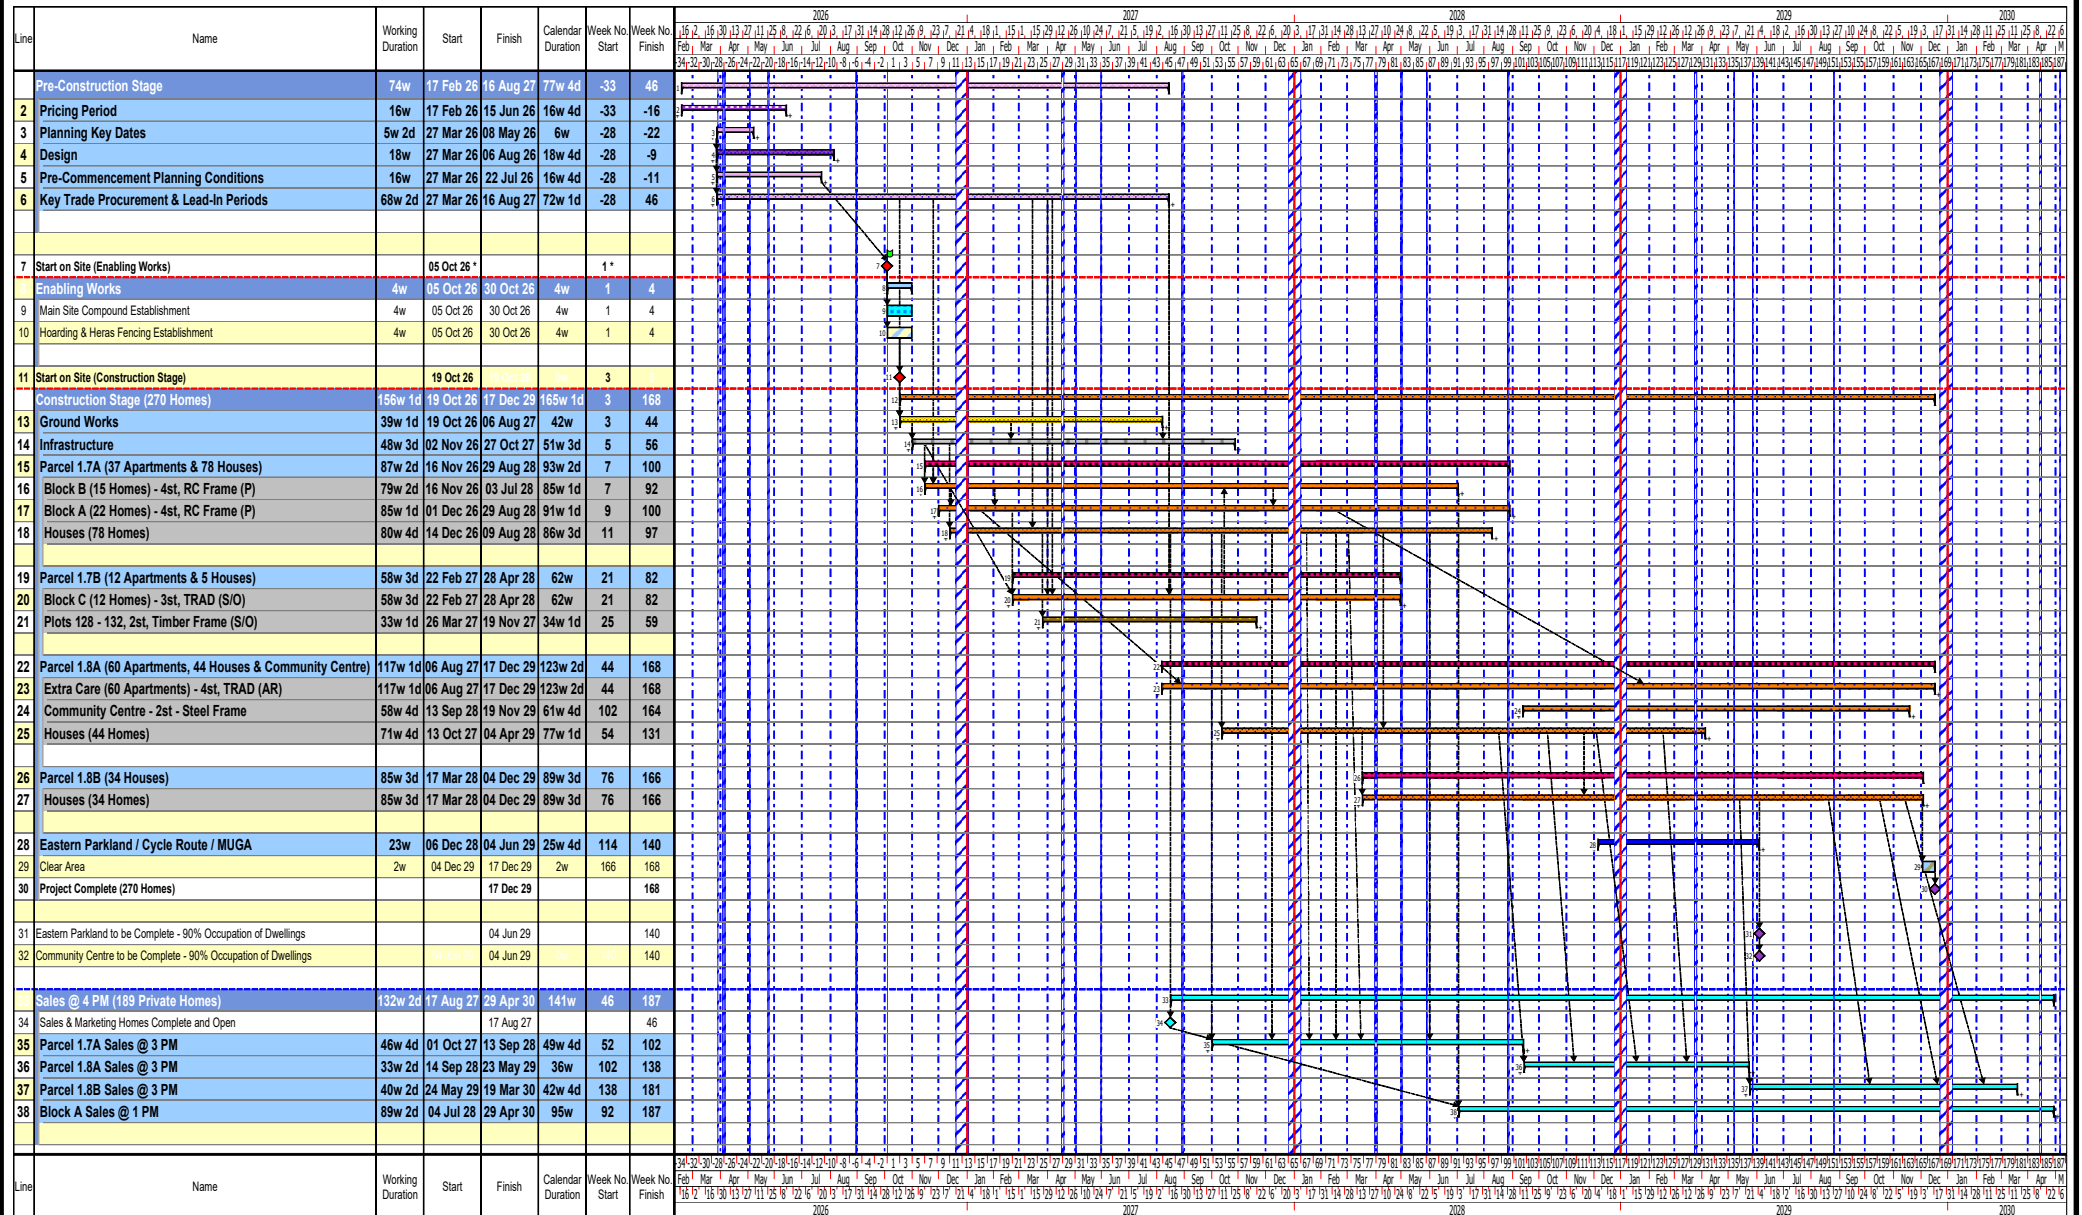

Prog. Number: 1
Revision: A

Issue Date: 25/06/2026
Revision Date:

Prog. Status: T22 118
Rev. Comment:

Appendix F

NORTHERN ARC, BURGESS HILL, PHASE 1C EASTERN NEIGHBOURHOOD

ECOLOGY STATEMENT FOR PARCEL 1.7A AND THE COMPOUND SITE - 1ST OCTOBER 2026

Mollie White - Assistant Ecologist

1. INTRODUCTION

1.1. In June 2026, a site walkover was conducted. The area of land that was surveyed is known as Northern Arc, Burgess Hill, Phase 1C, Eastern Neighborhood, hereafter this will be known as 'the Wider Site'. The grid reference for the center of the site is TQ 30967 20761.

1.2. This statement is for the partial discharge of Parcel 1.7A and the Compound Site from Condition 20 (only these areas and the remaining site is to be considered separately).

1.3. In an email from Mid Sussex District Council to the client dated 28th September 2026, the following was stated:

".... acknowledging that some parts of the site are more sensitive than others, we would be happy to partially discharge the conditions for each parcel, enabling you to commence on the plots where the surveys have been completed and the reports produced."

1.4. The Wider Site is 12.21 hectares (ha) in size, located north of Burgess Hill. The area looking for partial discharge includes Parcel 1.7A, which is approximately 4.01ha in size. The parcel is located in the northwest of the site with the A273 to the west and Holmbush Avenue to the south and the east. The habitats recorded within Parcel 1.7A are dominated by areas of bare ground, interspersed with areas of improved neutral grassland. A small area of hardstanding associated with a car park, established by previous developers. There is a tree located in the southwest of the site, this will not be impacted during the pre-commencement works.

1.5. The Compound Site is approximately 0.5ha in size. The Compound Site is located to the east of Holmbush Avenue. The main habitats present are bare ground as the dominant habitat and improved

neutral grassland.

- 1.6. Surveys are ongoing at the Wider Site; however, there is sufficient survey information and limited ecological value to Parcel 1.7A and the Site Compound where pre-commencement works are able to proceed pending approval.

2 METHODOLOGY

- 2.1. The site walkover was carried out on 8th June 2026 to identify habitats on the Wider Site and protected species that could be present
- 2.2. The UKHabs survey methodology was used to classify the habitat types in the Wider Site.
- 2.3. The Application Site habitats were compared to the habitats classified in the Biodiversity Statement and Metric Assessment by Middlemarch Environmental Ltd in 2025.¹
- 2.4. Notes of flora and fauna were made throughout the UKHabs survey onsite and were evaluated for their importance for supporting legally protected species.

¹ Middlemarch Environmental Ltd (2025). *Biodiversity Statement and Metric Assessment*.

HEAD OFFICE Rodbourne Rail Business Centre, Grange Lane, Malmesbury SN16 0ES t: 01666 825646
Unit 7, Godalming Business Centre, Woolsack Way, Godalming, GU7 1XW t: 01483 425714

mail@acdenv.co.uk

www.acdenvironmental.co.uk

Registered Office: Construction House, Runwell Road, Wickford, Essex SS11 7HQ

Co Reg No: 8058718 VAT No: 223888386





Figure 1: Approximate Red Line Site Boundary of the Wider Site (Google Earth 2026).



Figure 2: Approximate Red Line Site Boundary of Parcel 1.7A (Google Earth 2026)

HEAD OFFICE Rodbourne Rail Business Centre, Grange Lane, Malmesbury SN16 0ES t: 01666 825646
Unit 7, Godalming Business Centre, Woolsack Way, Godalming, GU7 1XW t: 01483 425714
mail@acdenv.co.uk
www.acdenvironmental.co.uk

Registered Office: Construction House, Runwell Road, Wickford, Essex SS11 7HQ
Co Reg No: 8058718 VAT No: 223888386





Figure 2: Approximate Red Line Site Boundary of Parcel 1.7A (Google Earth 2026)

2.5. This report has been written by Mollie White, Assistant Ecologist at ACD Environmental Ltd. She has experience carrying out a wide range of surveys including bat surveys, hazel dormouse *Muscardinus avellanarius* nest box and tube checks and reptile surveys. Mollie is a Qualifying Member of CIEEM. Mollie has also written a wide range of reports including Preliminary Ecological Appraisals (PEA), and Ecological Impact Assessments (EclA).

3 FAUNA

Bats

- 3.1. Within Parcel 1.7A, potential for bat roosting is limited to only one tree in the south of the parcel, which is a TPO tree and is not going to be impacted during the works. The hedgerow to the north of the parcel will be outside of the red line boundary; it may provide a commuting route, but it will not be impacted during the pre-commencement works.
- 3.2. The grassland in parcel 1.7A is unlikely to support foraging and commuting. The grassland has been removed due to archaeology works, and much of the site is bare ground and will have limited suitability

for foraging. The pre-commencing works are unlikely to affect the commuting routes as bats are more likely to be using the hedgerows outside of this area.

- 3.3. The Compound Site has no buildings/trees (in terms of consideration for roosting bats), the compound is to be placed on and areas of cleared grassland, there are trees located to the north and east of the Wider Site, but they will not be affected by the pre-commencement works, due to their distance from the compound. The foraging and commuting routes are unlikely to be affected by the pre-commencement works and the creation of the compound, because the area of grassland has already been cleared by other historical works that have been carried out on the site.
- 3.4. Bats have been considered on the Wider Site and mitigation will be in place for the remainder of the proposed works.
- 3.5. The pre-commencement work is unlikely to affect potential bat populations within the Wider Site.

Reptiles

- 3.6. If the presence of reptiles on site is confirmed, an appropriate mitigation and enhancement strategy should be developed.
- 3.7. Parcel 1.7A is unlikely to support reptiles; much of the site has been cleared for archeology works. The parcel contains small patches of grassland, scars from the digs and large piles of soil, from previous works. The hedgerow to the north could provide some suitable sheltering habitat although the hedgerow is not included in the red line and Heras fencing, which will be erected to protect the hedgerow and the roots of the trees.
- 3.8. The Compound Site is unlikely to support reptiles because there is minimal suitable habitat. As the area has previously been cleared, there is bare ground throughout most of the area, this is unsuitable for reptile foraging. The area has also been highly disturbed recently and reptiles are unlikely to be using the area for foraging.
- 3.9. Reptiles have been considered on the Wider Site and mitigation will be in place for the remainder of the proposed works.
- 3.10. The pre-commencement work is unlikely to affect potential reptile populations on the Wider Site.

Hazel dormouse

- 3.11. Parcel 1.7A is unlikely to support hazel dormouse. There is a record of a hazel dormouse from previous surveys carried out on the Wider Site and there is currently a hazel dormouse license for works being carried out on the east of the Wider Site by another consultancy. There is no suitable habitat within Parcel 1.7A. The hedgerow to the north of the parcel has potential to support hazel dormouse although the pre-commencement works will not affect the hedgerow and Heras fencing will be in place to protect the hedgerow and thus the hazel dormouse that could be using the hedgerow (albeit unlikely).
- 3.12. The Compound Site is unlikely to support hazel dormouse, due to a lack of supporting habitat and lack of connectivity. The Compound Site pre-commencement works are unlikely to impact hazel dormouse populations on the Wider Site.
- 3.13. Hazel dormouse have been considered on the Wider Site and mitigation will be in place for the remainder of the proposed works.

Birds

- 3.14. Parcel 1.7A is unlikely to support breeding birds, as there is limited suitable habitat for breeding birds. The majority of the parcels have been cleared, and bare ground is the dominant habitat, which is unsuitable for nesting birds. There is a tree located on the south of the site, this will not be impacted during the pre-commencement works and will be protected by Heras fencing. The hedgerow to the north will not be affected by the pre-commencement works as fencing will be in place to protect the hedgerow.
- 3.15. The Compound Site is also unlikely to support breeding birds due to the lack of suitable habitat. The pre-commencement works within the boundary of the compound site will not impact suitable areas within the Wider Site.
- 3.16. Breeding birds have been considered on the Wider Site and mitigation will be in place for the remainder of the proposed works.

Amphibians

- 3.17. Parcel 1.7A is unlikely to support great crested newt *Triturus cristatus* and common amphibians, due

HEAD OFFICE Rodbourne Rail Business Centre, Grange Lane, Malmesbury SN16 0ES t: 01666 825646
Unit 7, Godalming Business Centre, Woolsack Way, Godalming, GU7 1XW t: 01483 425714
mail@acdenv.co.uk
www.acdenvironmental.co.uk

to the lack of suitable habitat. There is limited habitat for the terrestrial phases for great crested newt and common amphibians. Due to the archeology works carried out on the parcel, there is limited terrestrial habitat.

3.18. The Compound Site is also unlikely to support newts and amphibians due to historical clearance of works that have been carried out. The Compound Site is predominantly bare ground, which is not suitable for the terrestrial phases for great crested newt and common amphibians.

3.19. The Wider Site is subject to a great crested newt District Level License (DLL) due to the potential for supporting newts and amphibians.

Badgers

3.20. Badgers *Meles meles* are present on the Wider Site with a badger sett in the north of the site. Parcel 1.7A is unlikely to support badgers as it fenced off, reducing the likelihood of badgers using the parcel for commuting or foraging.

3.21. The Compound Site is unlikely to support badgers, for foraging and commuting as there is limited suitable habitat.

3.22. No setts are present on Parcel 1.7A or the Compound Site.

3.23. The Wider Site had an active badger license for works being carried out in the woodland close to the sett.

Other mammals

3.24. Parcel 1.7A is unlikely to support other mammals, due to the lack of suitable foraging habitat and the disturbance which has taken place on the parcel. The parcel is also fenced off from the rest of the Wider Site reducing the likelihood of mammals such as foxes *Vulpes vulpes*, and hedgehogs *Erinaceus europaeus* using the parcel.

3.25. The Compound Site is unlikely to be used by mammals for foraging. The area may be used as a commuting route although there are better habitats for mammals to the east and south of the Compound Site.

3.26. No foxes or hedgehogs have been observed. No evidence of fox earths are present on Parcel 1.7A or the Compound Site.

Invertebrates

3.27. Parcel 1.7A is unlikely to support a significant assemblage of invertebrates and it is considered site level importance. As much of the parcels habitats have been removed and bare ground is the dominant habitat, it is unlikely invertebrates will be significantly impacted by the pre-commencement works.

3.28. The Compound Site is unlikely to support invertebrates, there is limited suitable habitat in the Compound Site, the pre-commencement works are unlikely to affect invertebrates on the Compound Site.

4 CONCLUSIONS

4.1. Parcel 1.7A has limited suitability for supporting protected species due to the limited habitats and fencing reducing the likelihood of species such as badger using the site. Much of parcel 1.7A is bare ground with rubble piles and archaeology scars and small patches of unimproved grassland.

4.2. The Compound Site has limited suitability due to the volume of bare ground and the historical works that have taken place on the Compound Site.

4.3. The proposed areas of pre-commencement works will not impact the rest of the Wider Site and mitigation will be implemented throughout the Wider Site due to the habitat and protected species potentially present.

4.4. It is considered that this report provides the information required for partial discharge of Condition 20 in relation to Parcel 1.7A and the Compound Site.

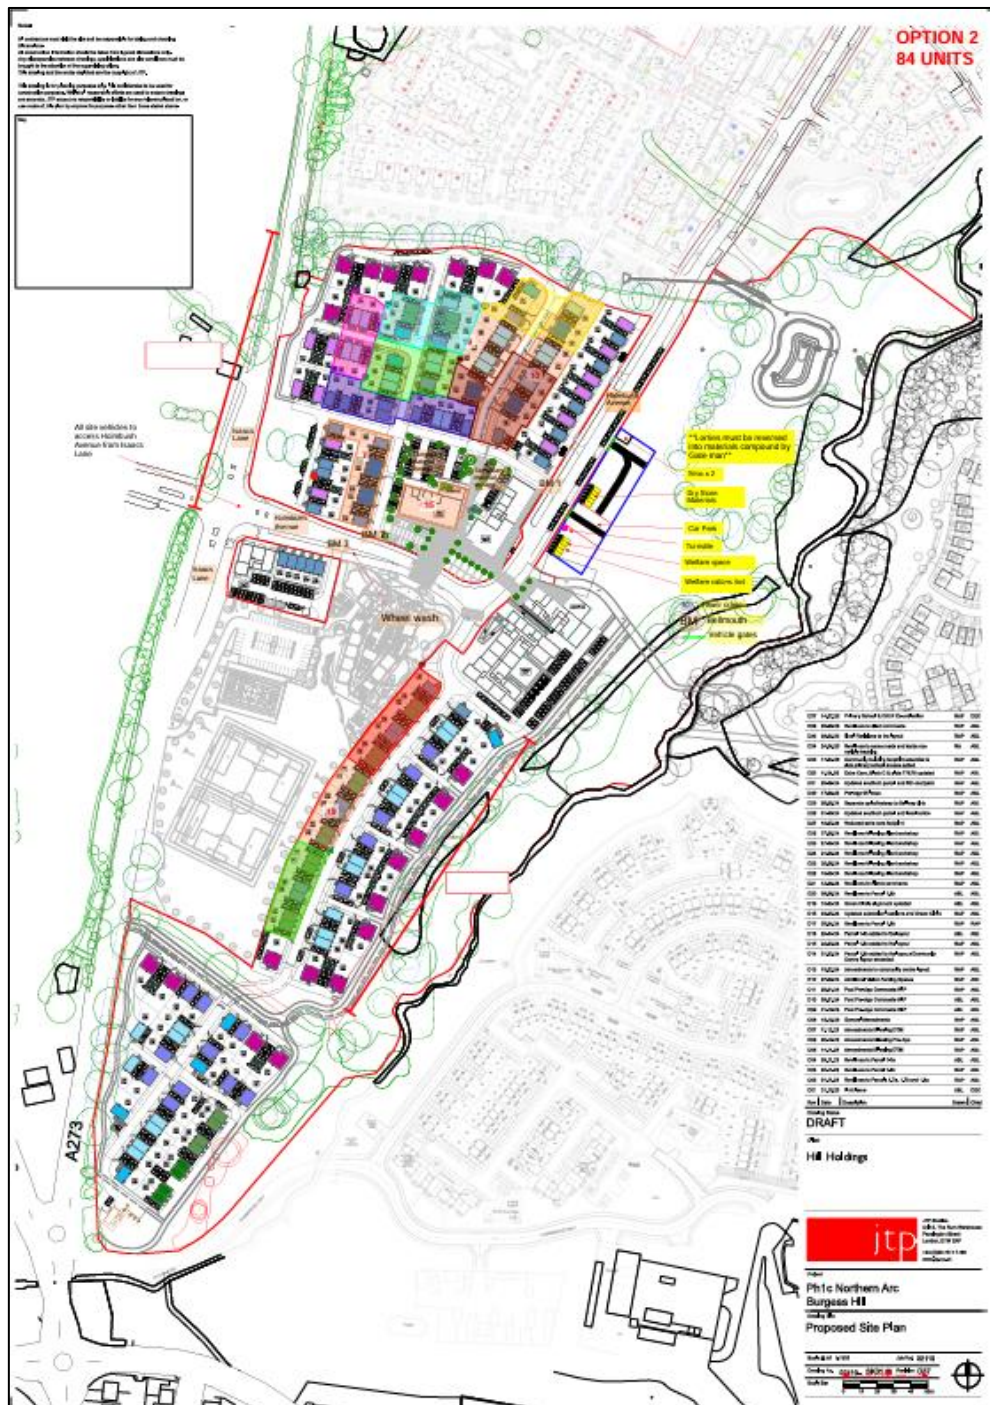


Figure 4: The Wider Site, Parcel 1.7A and Compound Site (Hill 2026)

HEAD OFFICE Rodbourne Rail Business Centre, Grange Lane, Malmesbury SN16 0ES t: 01666 825646
Unit 7, Godalming Business Centre, Woolsack Way, Godalming, GU7 1XW t: 01483 425714
mail@acdenv.co.uk
www.acdenvironmental.co.uk

Registered Office: ConstructionHouse, Runwell Road, Wickford, Essex SS11 7HQ
CoRegNo:8058718 VATNo:223888386
