

Indicative only

Tree Work Schedule		
No.	Species	Works
T09	Common Oak	Full to ground level and grind stump
G03	Veronica	Full to ground level and grind stump

All tree work to be undertaken in accordance with BS Standard BS 5898:2010 Tree work - Recommendations.  
All stumps are to be removed and the site is to be left as found. Care is to be taken of the ground around retained trees to make sure that it does not become compacted as a result of the surveying operations. No equipment or vehicles such as loader spades, tractors, excavators or cranes shall be parked or driven beneath the crowns of any retained trees, to prevent subsequent compaction and root death.

**Protective Fencing**

To be erected prior to the commencement of all works on site and retained in place throughout construction.  
Detailed Specification: To comprise either 2.4m wooden site hoarding or 2.3m high scaffolding framework comprising of vertical and horizontal framework, well braced to resist impacts, with uprights to be spaced at a maximum of 3.0m intervals and driven into the ground by a minimum of 600mm. On to this, standard anti-climb welded mesh panels are to be secured fixed to each other with at least two scaffold clamps and to the scaffold framework with wire.  
Separate Specification: To comprise of 2m tall welded mesh panels on rubber or concrete feet. Panels are to be joined together using a minimum of two anti-climb clamps, installed so that they can only be removed from inside the fence. The panels should be supported on the lower side by stabiliser struts, which should be attached to a base plate and secured with ground pins.  
All weather notices should be erected at regular intervals on the mesh panels with words such as "Construction exclusion zone - Keep out".

**Tree Protection Area KEEP OUT**  
Do not move this fence

TREES ENCLOSED BY THIS FENCE ARE PROTECTED BY PLANNING CONDITIONS AND ARE THE SUBJECT OF A TREE PRESERVATION ORDER. CONTRAVENTION OF A TREE PRESERVATION ORDER MAY LEAD TO CRIMINAL PROSECUTION.

ANY INCURSION INTO THE PROTECTED AREA MUST BE WITH THE WRITTEN PERMISSION OF THE LOCAL PLANNING AUTHORITY.

**Construction exclusion zone**

A construction exclusion zone (CEZ) is a designated area where there is to be no construction activity whatsoever. Access to the area for construction personnel or machinery is strictly prohibited and there is no scope for materials or waste storage etc.

**Arboricultural Supervision**

The arboricultural consultant will be required to attend site to directly supervise all demolition and construction works that have to be undertaken within the root protection areas. This will include:

1. Pre-commencement site meeting.
2. Location of protective measures.
3. Any demolition and/or excavations within or adjacent to RPA's e.g. underground services.
4. Arboricultural sign off and removal of protective measures.

**Arboricultural Method Statement**


Please refer to Arbtch Consulting Ltd. Tree Schedule and Arboricultural Method Statement, for full details on all surveyed trees and how all aspects of the development/works implemented without detriment to retained trees.

Note: New shared entrance created adjacent to tree T04 outside of the application boundary. Construction access will be via this entrance.

Protective fencing

Protective fencing: Existing fencing prevents access into the RPA of tree T04.

Protective fencing

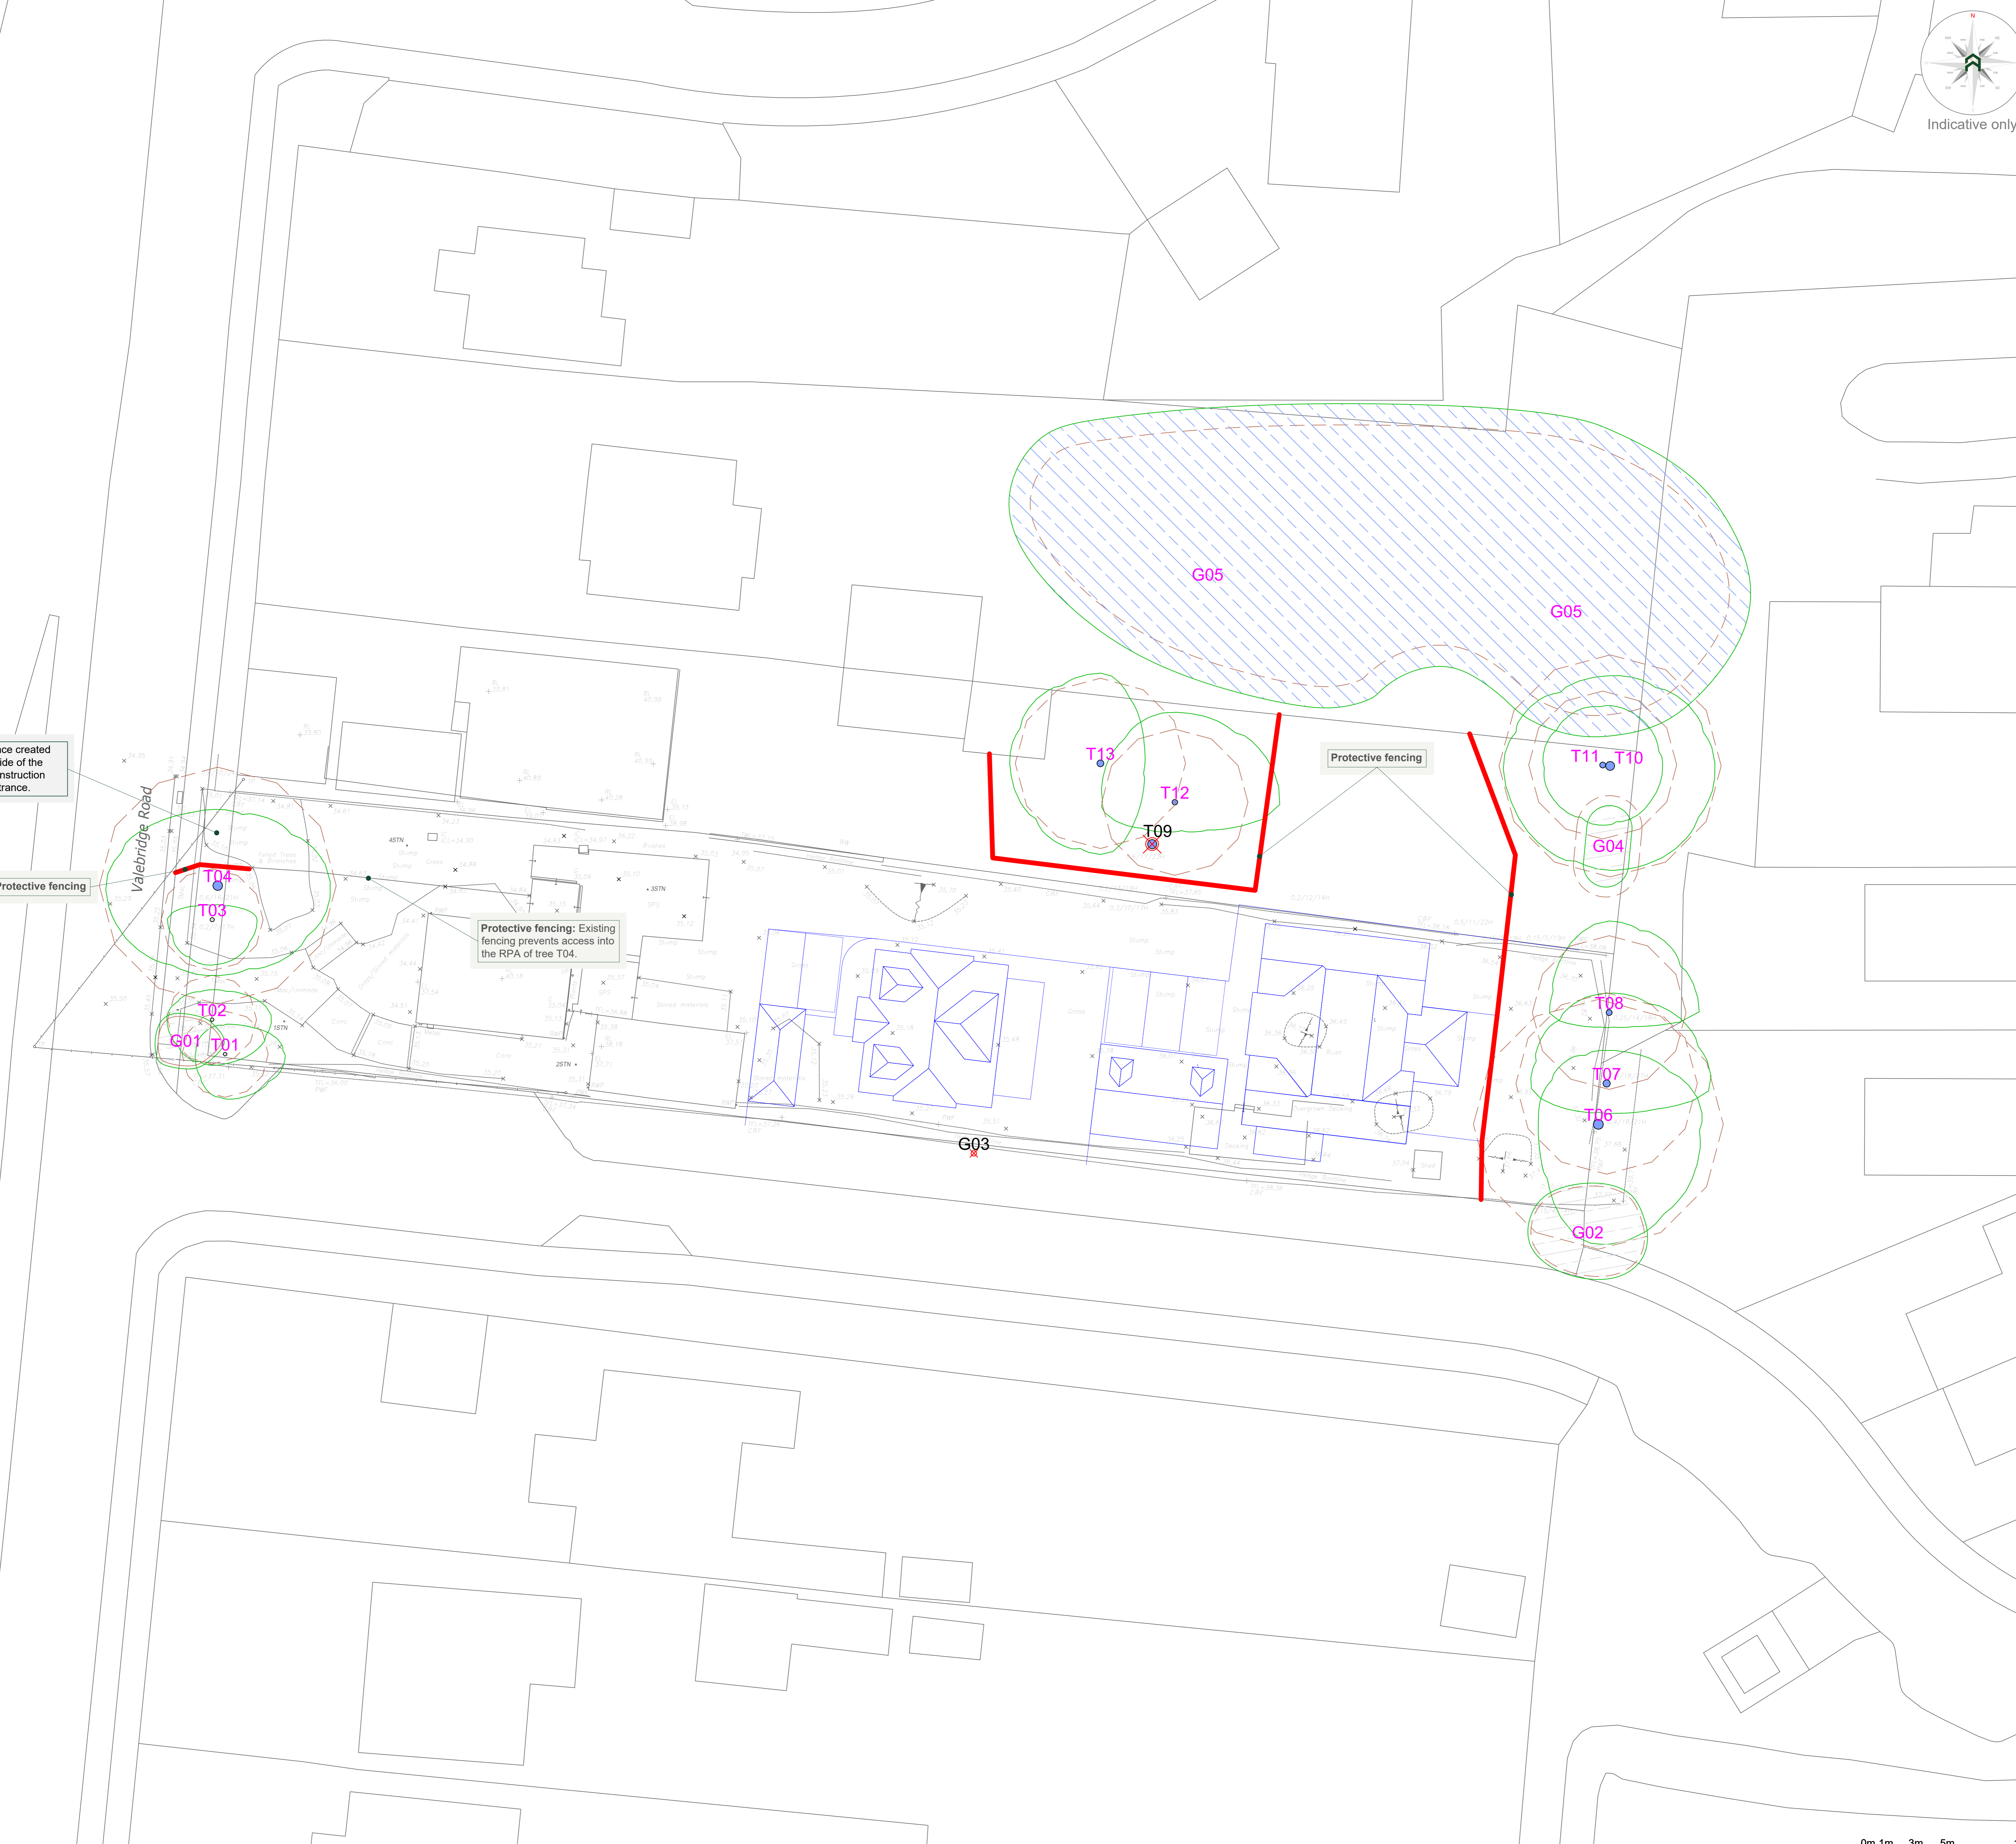

Project: Chideok, Valebridge Road, Burgess Hill, RH15 0RT

Client: Kauto Construction Ltd

Drawing: Tree Protection Plan

Based on: 2025-03-P-102

Drawing No: 44735969\_TPP02 Rev: 01

Date: Jan 2026 Scale: 1:150 @ A0 Drawn: FG

Key:

Tree Nos.:	T01	Tree Category:	Tree to be retained	Tree to be removed
RPA:	Category 'A' trees	Category 'B' trees	Category 'C' trees	Category 'D' trees
Protective fencing:	Existing	New	CEZ	CEZ

Please refer to Arbtch Consulting Ltd. Tree Schedule and Arboricultural Method Statement, for full details on all surveyed trees and how all aspects of the development/works implemented without detriment to retained trees.

The drawings are to be used as a guide only and do not constitute a contract. The drawings are the property of Arbtch Consulting Ltd. and shall remain the property of Arbtch Consulting Ltd. No part of these drawings may be reproduced or transmitted in any form or by any means electronic, mechanical, photocopying, recording, or by any information storage and retrieval system, without the prior written permission of Arbtch Consulting Ltd.

© Arbtch Consulting Ltd. 2026

