


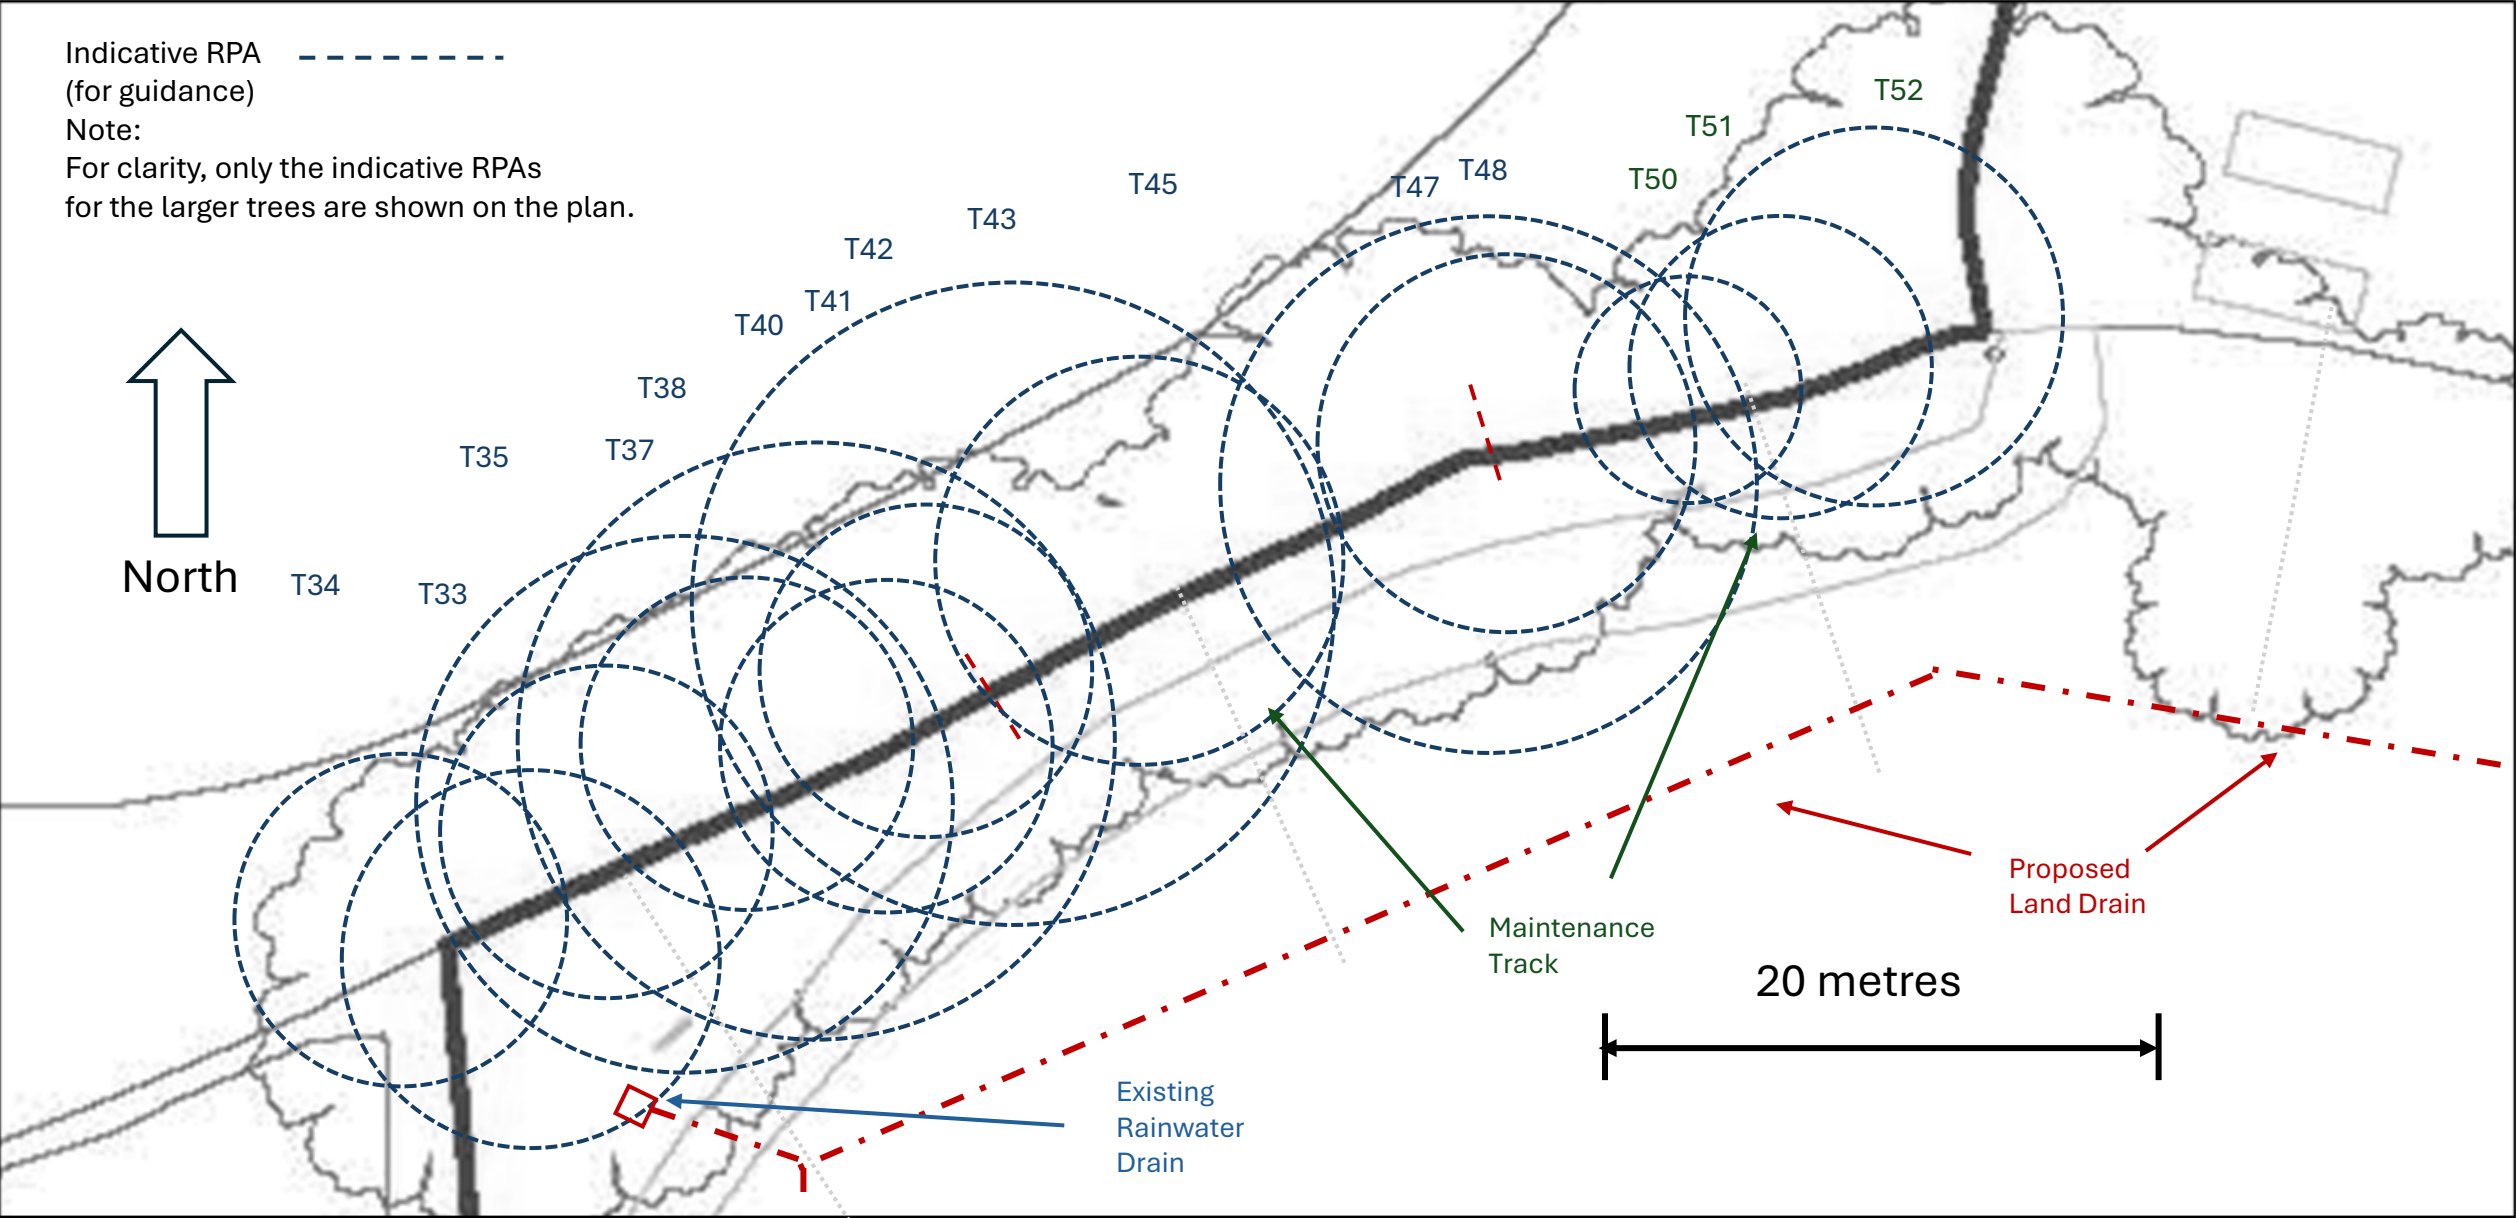

Tree Protection Notes

All trees shown on this plan are to be retained and protected.

Root Protection Areas (RPAs) are shown as construction exclusion zones. No excavation, soil disturbance, storage of materials, or machinery access shall occur within RPAs.

All plant and machinery associated with the works shall remain outside RPAs at all times.

The proposed **land drainage works are located outside RPAs** and will not require excavation within tree rooting areas.

Maintenance track works are limited to surface improvements above the existing track formation. The existing track base shall remain intact, and no excavation into undisturbed ground shall take place.

No materials, plant, fuel or spoil shall be stored within RPAs.

No mixing of cement, discharge of contaminants, or washing of equipment shall take place within RPAs.

Existing ground levels within RPAs shall not be altered.

Should any unforeseen requirement arise to excavate within the vicinity of retained trees, works shall cease in that area and advice shall be sought from a suitably qualified arboricultural consultant before works proceed.

All site operatives shall be briefed on the location of RPAs and tree protection requirements prior to commencement of works.
